

JASCOM DOG ADOPTION KENNEL REPLACEMENT

LACEY PROJECT NUMBER PW 2023-34

**SPECIFICATIONS AND BID DOCUMENTS
DEPARTMENT OF PUBLIC WORKS**

LACEY PROJECT NUMBER PW 2023-34

***CITY OF LACEY
WASHINGTON***

CITY OFFICIALS

MAYOR

ANDY RYDER

DEPUTY MAYOR

MALCOLM MILLER

COUNCIL MEMBERS

LENNY GREENSTEIN

MICHAEL STEADMAN

CAROLYN COX

ED KUNKEL

ROBIN VAZQUEZ

CITY MANAGER

RICK WALK

CITY ATTORNEY

DAVID S. SCHNEIDER

DIRECTOR OF PUBLIC WORKS

SCOTT EGGER, P.E.

CITY ENGINEER

AUBREY COLLIER, P.E., S.E.



**PUBLIC WORKS
DIRECTOR**

LACEY CONTRACT NUMBER PW 2023-34
CITY OF LACEY

I hereby certify that the Project Specifications were prepared by me or under my direct supervision and I am a duly registered Engineer under the laws of the state of Washington.

Ashley C. Smith
City of Lacey
Sections A, B, C, D, & F



TABLE OF CONTENTS

Advertisement for Bids	i
------------------------------	---

INSTRUCTIONS

Instructions to Bidders	A-1
Bidder's Checklist	A-2

BID DOCUMENTS

Proposal & Bid Sheet.....	B-1
Bid Bond Form	B-4
Non-Collusion Certificate.....	B-5
Certification of Compliance with Wage Payment Statutes.....	B-6

CONTRACT DOCUMENTS

Construction Contract	C-1
Performance Bond Form.....	C-4
Declaration of Option for Management of Statutory Retained Percentage.	C-6

AMENDMENTS AND SPECIAL PROVISIONS

Table of Contents	ii
Amendments	D-1
Special Provisions	D-2
APPENDIX A	D-35
APPENDIX B	D-43
APPENDIX C	D-49

TECHNICAL SPECIFICATIONS – PART E

Kennel Specifications	E-2
-----------------------------	-----

PREVAILING MINIMUM HOURLY RATES

State Wage Rates	F-1
------------------------	-----

A INSTRUCTIONS

INSTRUCTIONS TO BIDDERS

Bidders shall examine contract and bid documents and the site and shall satisfy themselves as to conditions that exist.

Each Bidder shall submit to the City Clerk, Lacey, Washington a sealed bid endorsed upon the outside wrapper with **JASCOM DOG ADOPTION KENNEL REPLACEMENT** at the time and place designated in the advertisement.

Bids may be delivered in person to Lacey City Hall, 420 College Street SE, or by mail to City of Lacey 420 College St SE Lacey, WA 98503.

The City of Lacey is committed to offering reasonable accommodations to persons with disabilities. We invite any person with special needs to contact the City Clerk at (360) 491-3212 at least seventy-two (72) hours before the meeting to discuss any special accommodations that may be necessary. Citizens with hearing impairment may call the TDD line at (800) 833-6388.

Each Bidder shall complete the proposal with prices in figures with the extension properly computed. The proposal must be properly signed by a duly authorized agent. Proposal must acknowledge addenda, if any, received.

If alternates are included in the proposal the Bidder shall complete the alternates. The City will award the contract to the lowest responsible Bidder as determined by the Special Provisions. The City reserves the right to delete alternates after award.

A Bidder will be deemed not responsible if the Bidder does not meet the mandatory bidder responsibility criteria in RCW 39.04.350(1).

The City does not pre-qualify Bidders. However, if the apparent low Bidder has not already been determined qualified, the City shall afford seven (7) days after notification for the low Bidder to provide evidence for evaluation, as to capability to perform the work. The evaluation will include consideration of experience, personnel, equipment, financial resources as well as performance record. The information must be sufficient to enable the Bidder to obtain the required qualification rating prior to the award of the contract.

No bidder may withdraw his bid after the hour set for the opening of bids or before award of the contract unless said award is delayed for a period of forty-five (45) days.

CONTRACT PARTS

The contract to be executed as a result of this bid consists of multiple parts, all of which pertain as if fully attached hereto and Bidder shall consider all parts as a complete document. In the event of discrepancies between the various parts, precedent shall be in the following order:

1. Contract Form,
 2. Addenda (if any),
 3. Proposal Form,
 4. Special Provisions,
 5. Technical Specifications, if included,
 6. Contract Plans,
 7. WSDOT Standard Specifications for Road, Bridge, and Municipal Construction,
 8. City of Lacey Development Guidelines and Public Works Standards, and
 9. WSDOT Standard Plans for Road, Bridge and Municipal Construction
- The Bidder is directed to complete and return the forms in Section B as a bid proposal.

BIDDER'S CHECKLIST

The bidder's attention is especially called to the following forms which must be executed in full as required, and submitted with the bid proposal:

1. Proposal: The unit prices bid must be shown in the space provided.
2. Proposal Signature Sheet: To be filled in and signed by the bidder. All addenda must be acknowledged.
3. Bid Deposit: Any bid shall be accompanied by a deposit of cash, certified check, cashier's check, or surety bond, in an amount equal to at least five percent (5%) of the total amount bid. Checks shall be payable to the City Clerk, City of Lacey, Washington.

If a surety bond is used, it shall be submitted on a form furnished by the Commission and signed by the bidder and his surety company. The sureties' "attorney-in-fact" must be registered with the Washington State Insurance Commissioner. The power of attorney must also be submitted with the bond. See Specification section 1-02.7 for more information.

4. Non-Collusion and Debarment Affidavit

The following form must be submitted within 24 hours following the bid submittal deadlines.

5. Certification of Compliance with Wage Payment Statutes

The following must be completed before the contract can be awarded:

6. L&I training on the requirements related to public works and prevailing wages per RCW 39.04.350
7. Certification of Employment Security Department (ESD) good standing

The following forms are to be executed after the contract is awarded:

8. Contract: This agreement to be executed by the successful bidder
9. Performance and Payment Bond
10. Insurance Certificate

Bidder's Checklist

1. Proposal
2. Proposal Signature Sheet
Addenda Acknowledged
3. Bid Deposit
Power of Attorney included if applicable
4. Non-Collusion and Debarment Affidavit
5. Certification of Compliance with Wage Payment Statutes
6. L&I Public Works Prevailing Wage Training
7. ESD Certification

B

BID DOCUMENTS

CITY OF LACEY

JASCOM Dog Adoption Kennel Replacement

Lacey Contract Number: PW 2023-34
Federal Aid Project Number:
WSDOT Contract Number:
TIB Contract Number:

Contract Proposal

DATE: _____

The undersigned, as bidder, has examined the bid documents as prepared by the Public Works Department, City of Lacey.

The undersigned, as bidder, proposes to furnish all material and perform all labor in accordance with the bid documents at the following prices.

Bidder must fill in unit prices in figures for each item and total.

Bidder shall sign this proposal form and submit all required paperwork with the bid.

A General						
No.	Quantity	Unit	Item ID	Item Description	Unit Price	Extended Price
A1	17000	MC	104-010	Minor Change	\$1.00	\$17,000.00
A2	1	LS	109-010	Mobilization	LUMP SUM	
A3	1	LS	850-792	Project Closeout	\$500.00	\$500.00
A4	1	LS	895-505	Building Improvement	LUMP SUM	
Schedule A Subtotal:						
Tax Rate (%) : 9.50 Tax:						
Schedule A Total:						
Contract Total:						
(All Schedules)						

The undersigned also agrees as follows:

- Within 10 calendar days after the contract is awarded to sign and return the contract and provide insurance documents.
- That this proposal cannot be withdrawn within 45 days after receipt of bids.
- That it is the understanding that the City of Lacey may accept or reject any or all bids.
- The undersigned hereby agrees to pay for labor not less than the prevailing rates of wages per the bid documents.
- Enclosed with this proposal is a bid deposit in the sum of 5% of the bid total amount which it is agreed shall be collected and retained by the City of Lacey as liquidated damages in the event this proposal is accepted by the City of Lacey with 45 calendar days after the receipt of bids and the undersigned fails to execute the contract and the required bond with the City of Lacey, under the conditions thereof, within 10 calendar days after the undersigned is notified that said proposal has been accepted, otherwise said bid deposit shall be returned to the undersigned upon demand.
- A Performance/Payment Bond will be furnished to the City with the contract.
- Retention will be held on this contract per RCW 60.28.011.

Addenda Receipt Acknowledged

Signature of Bidder Date
(If an Individual, Partnership, or Non-Incorporated organization)

Firm Name Please Print Phone

Address of Bidder: _____

Name and Address of Firm Members:

Signature of Bidder (if a Corporation)
Title: _____

Firm Name: _____ Phone: _____

Business Address: _____

Incorporated under the Laws of the State of _____

Officers	Address
President: _____	_____
Secretary: _____	_____
Treasurer: _____	_____

BID DEPOSIT SELECTION

A bid deposit in an amount of five percent (5%) of the total bid amount is attached hereto:

CASH ☐ In the amount of _____

CASHIER'S CHECK ☐ In the amount of _____

CERTIFIED CHECK ☐ In the amount of _____

BID BOND ☐ In the amount of 5% of the total bid amount

**CONTRACTOR'S BID DEPOSIT SURETY BOND
to City of Lacey, Washington**

We, _____, as Principal, existing under and by virtue of the laws of the State of Washington and authorized to do business in the State of Washington, and _____, as Surety, organized and existing under the laws of the State of _____, are held and firmly bound unto the City of Lacey, a Washington municipality, as Obligee, in the penal sum of 5% of the total amount bid, not to exceed \$ _____, for the payment of which we jointly and severally bind ourselves, and our legal representatives and successors.

WHEREAS, the Principal has submitted a bid for **JASCOM DOG ADOPTION KENNEL REPLACEMENT**.

NOW THEREFORE, the condition of the obligation is such that if the Obligee shall accept the bid of Principal and make timely award to the Principal according to the terms of the bid documents; and the Principal shall, within ten days after notice of the award, exclusive of the day of notice, enter into the contract with the Obligee and furnish the contractor's bonds (performance and payment bonds) with Surety satisfactory to the Obligee in an amount equal to 100% of the amount of the bid proposed including additives, alternatives and Washington State sales tax, then this obligation shall be null and void; otherwise if the Principal fails to enter into the contract and fails to furnish the contractor's bonds within ten days of notice of award, exclusive of the day of notice, the amount of the bid deposit shall be forfeited to the Obligee, payable by the Surety; but in no event will the Surety's liability exceed the face amount of this bid bond.

This bond may be executed in two original counterparts, and shall be signed by the parties' duly authorized officers. This bond will only be accepted if it is accompanied by a fully executed and original power of attorney for the officer executing on behalf of the surety.

PRINCIPAL (CONTRACTOR)

SURETY

Principal Signature Date

Surety Signature Date

Printed Name

Printed Name

Title

Title

Name, address, and telephone of local office/agent of Surety Company is:

NON-COLLUSION AND DEBARMENT AFFIDAVIT

State of _____)

)ss

County of _____)

I, the undersigned, being duly sworn, deposes and says that the person, firm, association, copartnership or corporation herein named, has not either directly or indirectly, entered into any agreement, participated in any collusion, or otherwise taken any action in restraint of free competitive bidding in the preparation and submission of a proposal of the City of Lacey for consideration in the award of a contract on the improvement described as follows.

I further certify that, except as noted below, the firm, association or corporation or any person in a controlling capacity associated therewith or any position involving the administration of State or federal funds; is not currently under suspension, debarment, voluntary exclusion, or determination of ineligibility by any federal or State agency; has not been suspended, debarred, voluntarily excluded or determined ineligible by any federal or State agency within the past three years; does not have a proposed debarment pending; and has not been indicted, convicted, or had a civil judgment rendered against said person, firm, association or corporation by a court of competent jurisdiction in any matter involving fraud or official misconduct within the past three years.

I further acknowledge that by signing my signature, I am deemed to have signed and have agreed to the provisions of this affidavit.

Name of Project

Name of Firm

Signature of Authorized Member

Sworn to before me this

_____ day of _____, 20 _____

Notary Public

(CORPORATE SEAL)

CERTIFICATION OF COMPLIANCE WITH WAGE PAYMENT STATUTES

The bidder hereby certifies that, within the three-year period immediately preceding the bid solicitation date, the bidder is not a “willful” violator, as defined in RCW 49.48.082, of any provision of chapters 49.46, 49.48, or 49.52 RCW, as determined by a final and binding citation and notice of assessment issued by the Department of Labor and Industries or through a civil judgment entered by a court of limited or general jurisdiction.

I certify under penalty of perjury under the laws of the State of Washington that the foregoing is true and correct.

Bidder’s Business Name

Signature of Authorized Official*

Printed Name

Title

Date

City

State

Check One:

Sole Proprietorship ☐ Partnership ☐ Joint Venture ☐ Corporation ☐

State of Incorporation, or if not a corporation, State where business entity was formed:

If a co-partnership, give firm name under which business is transacted:

** If a corporation, proposal must be executed in the corporate name by the president or vice-president (or any other corporate officer accompanied by evidence of authority to sign). If a co-partnership, proposal must be executed by a partner.*

This form must be submitted with the Bid Proposal or as a Supplement to the Bid no later than 24 hours after the time for delivery of the Bid Proposal, as provided for in Section 1-02.9 of the Contract Provisions.

**CERTIFICATION OF EMPLOYMENT SECURITY DEPARTMENT (ESD)
GOOD STANDING AND NUMBER**

The bidder hereby provides an ESD number and certifies that per RCW 39.04.350 and Title 50 RCW, in which the City will verify prior to entering into contract with the Contractor, that the Bidder has a valid ESD number and is deemed to be in good standing with Washington State's Employment Security Department.

I certify under penalty of perjury under the laws of the State of Washington that the foregoing is true and correct.

Bidder's Business Name

Employment Security Department (ESD) Number

WA State Unified Business Identifier (UBI #)

Signature of Authorized Official*

Printed Name

Title

Date

City

State

.

C CONTRACT DOCUMENTS

CONSTRUCTION CONTRACT

THIS AGREEMENT, made and effective as of the date of the last signature below, between the City of Lacey, hereinafter called Owner, under and by virtue of the charter, laws and ordinances of the said Owner and the laws of the State of Washington, and

_____ hereinafter called Contractor,

WITNESSETH:

That in consideration of the payment, covenants and agreement hereinafter mentioned, attached and made a part of this Agreement, to be made and performed by the parties hereto, the parties covenant and agree as follows regarding:

City of Lacey Contract No. PW 2023-34 for the “**JASCOM DOG ADOPTION KENNEL REPLACEMENT**” project in the sum of:

_____ Dollars (\$ _____)

including applicable sales tax.

1. The Contractor shall do all work and furnish all tools, materials and equipment in accordance with and as described in the attached Plans and Specifications, and in full compliance with the terms, conditions and stipulations herein set forth and attached, now referred to and by such reference incorporated herein and made a part hereof as fully for all purposes as if here set forth at length, and shall perform any alterations in or in addition to the work covered by this Contract and every part thereof and any force account work which may be ordered as provided in this Contract and every part thereof.

The Contractor shall provide and bear the expense of all materials, labor, equipment, tools, implements and conveniences and things of every description that may be requisite for the transfer of materials and for constructing and completing the work provided for in this Contract and every part thereof, except such as are mentioned in the Specifications to be furnished by the Owner.

2. The Owner hereby promises and agrees with the Contractor to employ, and does employ the Contractor to provide the materials and to do and cause to be done the above described work and to complete and finish the same according to the attached Plans and Specifications and the schedule of unit or itemized prices hereto attached, at the time and in the manner and upon the conditions provided for in this Contract and every part thereof.
3. Contractor, for himself and for his heirs, executors, administrators, successors, assigns, does hereby agree to the full performance of all the covenants herein contained upon the part of Contractor.
4. It is further provided that no liability shall attach to Owner or Agent thereof by reason of entering into this Contract, except as expressly provided herein.

5. Payments will be made under the Contract according to the schedule of rates and prices and the specification attached and made a part thereof. Partial payments under the Contract will be made at the request of the Contractor not more than once each month upon approval of the Owner, as hereinafter specified, provided they are in accordance with the provisions of RCW 60.28.010. There will be reserved and retained from monies earned by the Contractor, as determined by such monthly estimates, a sum equal to 5 percent of the Contract price.

Payment of the retained percentage shall be withheld for a period of forty-five (45) days following the final acceptance of the work and materials by the Owner, and shall be paid the Contractor at the expiration of said forty-five (45) days in event no claims, as provided by law, have been filed against such funds; and provided further, that releases have been obtained from all departments and agencies having jurisdiction over the activities of the Contractor. In the event such claims are filed, Contractor shall be paid such retained percentages less an amount sufficient to pay any such claims together with a sum sufficient to pay the cost of such action, and to cover attorney fees as determined by the Owner.

6. Requests for review of substitute items of material or equipment will not be accepted by the Owner or Agent from anyone other than the Contractor. If the Contractor wishes to furnish a substitute item, the Contractor shall make written application to the Owner's Agent for acceptance thereof, certifying that the proposed substitute will perform adequately the functions called for by the general design, be similar and of equal substance to that specified and be suited to the same use and capable of performing the same function as that specified. All variations of the proposed substitute from that specified shall be identified in the application and available maintenance, repair and replacement service will be indicated. The application will also contain an itemized estimate of all costs that will result directly or indirectly from acceptance of such substitute, which shall be considered by the Owner in evaluating the proposed substitute. The Owner may require the Contractor to furnish at the Contractor's expense, additional data about the proposed substitute. The Owner will be the sole judge of acceptability, and no substitute will be ordered without the Owner's prior written acceptance. The Owner may require the Contractor to furnish at the Contractor's expense, a special performance guarantee or other surety with respect to any other substitute.

The Owner or Agent will record the time and expenses in evaluating substitutions proposed by the Contractor. Whether or not the Owner accepts a proposed substitute, the Contractor shall reimburse the Owner for the costs of evaluating any proposed substitute.

7. The Owner reserves the right, after the final payment has been made, to claim and recover by process of law such sums as may be sufficient to make good any defects in the equipment or to recover any over-payment resulting from dishonest acts of the Contractor.
8. The contract time will commence to run, and the Contractor shall start to perform his obligation under the contract documents, on the day indicated in the Notice to Proceed given by Owner to Contractor; but in no event shall contract time commence to run later than the 30th calendar day after the date when both Owner and Contractor execute the Contract. A Notice to Proceed may be given at any time within thirty (30) calendar days after the date when both Owner and Contractor execute the Contract.

9. The Contractor shall guarantee the materials and workmanship for a period of one (1) year from and after the date of final acceptance by the Owner.

If, within said guarantee period, repairs are required which, in the opinion of the Owner, are rendered necessary as a result of work or materials which are inferior, defective or not in accordance with the terms of the Contract, the Contractor shall, promptly upon receipt of notice from the Owner, and without expense to the Owner, (a) correct all defects and place in satisfactory condition in every particular all of such guaranteed work and materials; (b) make good all damage which in the opinion of the Owner is caused by such defects; and (c) make good any other work or material or the equipment and contents of a building, structure or site disturbed in fulfilling any such guarantee.

If the Contractor, after notice, fails within ten (10) days to proceed to comply to the terms of this guarantee, the Owner may have the defects corrected, and the Contractor and his Surety shall be liable for all expense incurred, provided, however, that in case of an emergency where, in the opinion of the Owner, delay would cause serious loss or damage, repairs may be made without notice being given to the Contractor and the Contractor shall pay the cost thereof.

IN WITNESS WHEREOF, the said Contractor has executed this instrument and the City Manager, pursuant to resolution duly adopted, has caused this instrument to be executed in the name of the City of Lacey the day and year first above-written.

Contractor

Date

Contractor's Registration Number (UBI No.)

City of Lacey Business License Number

City Manager

Date

ATTEST:

By:

City Clerk

APPROVED AS TO FORM:

By :

City Attorney

**CONTRACTOR'S PERFORMANCE/PAYMENT BOND
to City of Lacey, Washington**

The City of Lacey, Washington, in Thurston County, has awarded to _____ (Contractor), as Principal, a contract for the construction of the project designated as **JASCOM DOG ADDOPTION KENNEL REPLACEMENT**, Project No. **Project #2023-34** in Lacey, Washington, and said Principal is required under the terms of the Contract to furnish a performance/payment bond in accordance with chapter 39.08 Revised Code of Washington (RCW).

The Principal, and _____ (Surety), a corporation, organized under the laws of _____ and licensed to do business in the State of Washington as surety and named in the current list of "Surety Companies Acceptable in Federal Bonds" as published in the Federal Register by the Audit Staff Bureau of Accounts, U.S. Treasury Dept., are jointly and severally held and firmly bound to the City of Lacey, as Obligee, in the sum of \$ _____ total Contract amount (including Washington State sales tax), subject to the provisions herein.

The obligations of this bond shall become null and void, if and when the Principal, its heirs, executors, administrators, successors, or assigns shall well and faithfully perform all of the Principal's obligations under the Contract and fulfill all the terms and conditions of all duly authorized modifications, additions, and changes to said Contract that may hereafter be made, at the time and in the manner therein specified; shall pay all persons in accordance with chapters 39.08, 39.12, and 60.28 RCW, including all workers, laborers, mechanics, subcontractors, and material suppliers, and all persons who shall supply such contractor or subcontractor with provisions and supplies for the carrying on of such work; shall warranty the work as provided in the Contract and shall indemnify and hold harmless the Obligee from any defects in the workmanship and materials incorporated into the work for the period identified in the Contract; and if such obligations have not been fulfilled, this bond shall remain in full force and effect.

The Surety for value received agrees that no change, extension of time, alteration or addition to the terms of the Contract, the specifications accompanying the Contract, or to the work to be performed under the Contract shall in any way affect its obligation on this bond, and waives notice of any change, extension of time, alteration or addition to the terms of the Contract or the work performed. The Surety agrees that modifications and changes to the terms and conditions of the Contract that increase the total amount to be paid the Principal shall automatically increase the obligation of the Surety on this bond and notice to Surety is not required for such increased obligation.

This bond may be executed in two original counterparts and shall be signed by the parties' duly authorized officers. This bond will only be accepted if it is accompanied by a fully executed and original power of attorney for the officer executing on behalf of the surety.

PRINCIPAL (CONTRACTOR)

SURETY

Principal Signature

Date

Surety Signature

Date

Printed Name

Printed Name

Title

Title

Name, address, and telephone of local office/agent of Surety Company is:

**DECLARATION OF OPTION FOR MANAGEMENT OF
STATUTORY RETAINED PERCENTAGE**

- A. I hereby elect to have the retained percentage of this contract held in a fund by the City of Lacey until forty-five (45) days following final acceptance of the work.

Contractor (please print)

Date

Signature

- B. I hereby elect to have the City of Lacey invest the retained percentage of this contract from time to time as such retained percentage accrues and in accordance with RCW Ch. 60.28.

I hereby designate _____ as the repository for the escrow of said funds.

I hereby further agree to be fully responsible for payment of all costs or fees incurred as a result of placing said percentage in escrow and investing it as authorized by statute.

The City of Lacey shall not be liable in any way for any costs or fees in connection therewith.

Contractor (please print)

Date

Signature

- C. I hereby elect to hold a retainage bond.

Contractor (please print)

Date

Signature

D
SPECIAL
PROVISIONS

TABLE OF CONTENTS

SPECIAL PROVISIONS	2
INTRODUCTION TO THE SPECIAL PROVISIONS	2
DESCRIPTION OF WORK	2
1-01 DEFINITIONS AND TERMS	2
1-02 BID PROCEDURES AND CONDITIONS	4
1-03 AWARD AND EXECUTION OF CONTRACT	9
1-04 SCOPE OF THE WORK	12
1-05 CONTROL OF WORK	13
1-06 CONTROL OF MATERIAL	17
1-07 LEGAL RELATIONS AND RESPONSIBILITIES TO THE PUBLIC.....	18
1-08 PROSECUTION AND PROGRESS	23
1-09 MEASUREMENT AND PAYMENT	28
8-50 MISCELLANEOUS.....	31
8-51 BUILDING IMPROVEMENTS.....	32
APPENDIX A - COL RAM FROM & INSTRUCTIONS.....	35
APPENDIX B - PLANS AND AS-BUILTS	43
APPENDIX C - SITE PHOTOS.....	49

SPECIAL PROVISIONS

INTRODUCTION TO THE SPECIAL PROVISIONS

(January 19, 2022 APWA GSP)

The work on this project shall be accomplished in accordance with the *Standard Specifications for Road, Bridge and Municipal Construction*, 2023 edition, as issued by the Washington State Department of Transportation (WSDOT) and the American Public Works Association (APWA), Washington State Chapter (hereafter “Standard Specifications”). The Standard Specifications, as modified or supplemented by these Special Provisions, all of which are made a part of the Contract Documents, shall govern all of the Work.

These Special Provisions are made up of both General Special Provisions (GSPs) from various sources, which may have project-specific fill-ins; and project-specific Special Provisions. Each Provision either supplements, modifies, or replaces the comparable Standard Specification, or is a new Provision. The deletion, amendment, alteration, or addition to any subsection or portion of the Standard Specifications is meant to pertain only to that particular portion of the section, and in no way should it be interpreted that the balance of the section does not apply.

The project-specific Special Provisions are not labeled as such, but are generally denoted with (*****). The GSPs are labeled under the headers of each GSP, with the effective date of the GSP and its source, except WSDOT uses a date only (2nd on list). For example:

(March 8, 2013 APWA GSP)
(April 1, 2013)
(May 1, 2013 Lacey GSP)

Also incorporated into the Contract Documents by reference are:

- *Manual on Uniform Traffic Control Devices for Streets and Highways*, currently adopted edition, with Washington State modifications, if any
- *Standard Plans for Road, Bridge and Municipal Construction*, WSDOT/APWA, current edition
- City of Lacey Development Guidelines and Public Works Standards, current edition

Contractor shall obtain copies of these publications, at Contractor’s own expense.

DESCRIPTION OF WORK

This contract provides for the removal and disposal of the 18 existing kennels as well as furnishing and completely installing 18 new kennels including drain lines and all other incidental work.

1-01 DEFINITIONS AND TERMS

1-01.3 Definitions

(January 19, 2022 APWA GSP)

Delete the heading Completion Dates and the three paragraphs that follow it, and replace them with the following:

Dates

Bid Opening Date

The date on which the Contracting Agency publicly opens and reads the Bids.

Award Date

The date of the formal decision of the Contracting Agency to accept the lowest responsible and responsive Bidder for the Work.

Contract Execution Date

The date the Contracting Agency officially binds the Agency to the Contract.

Notice to Proceed Date

The date stated in the Notice to Proceed on which the Contract time begins.

Substantial Completion Date

The day the Engineer determines the Contracting Agency has full and unrestricted use and benefit of the facilities, both from the operational and safety standpoint, any remaining traffic disruptions will be rare and brief, and only minor incidental work, replacement of temporary substitute facilities, plant establishment periods, or correction or repair remains for the Physical Completion of the total Contract.

Physical Completion Date

The day all of the Work is physically completed on the project. All documentation required by the Contract and required by law does not necessarily need to be furnished by the Contractor by this date.

Completion Date

The day all the Work specified in the Contract is completed and all the obligations of the Contractor under the contract are fulfilled by the Contractor. All documentation required by the Contract and required by law must be furnished by the Contractor before establishment of this date.

Final Acceptance Date

The date on which the Contracting Agency accepts the Work as complete.

Supplement this Section with the following:

All references in the Standard Specifications or WSDOT General Special Provisions, to the terms “Department of Transportation”, “Washington State Transportation Commission”, “Commission”, “Secretary of Transportation”, “Secretary”, “Headquarters”, and “State Treasurer” shall be revised to read “Contracting Agency”.

All references to the terms “State” or “state” shall be revised to read “Contracting Agency” unless the reference is to an administrative agency of the State of Washington, a State statute or regulation, or the context reasonably indicates otherwise.

All references to “State Materials Laboratory” shall be revised to read “Contracting Agency designated location”.

All references to “final contract voucher certification” shall be interpreted to mean the Contracting Agency form(s) by which final payment is authorized, and final completion and acceptance granted.

Additive

A supplemental unit of work or group of bid items, identified separately in the Bid Proposal, which may, at the discretion of the Contracting Agency, be awarded in addition to the base bid.

Alternate

One of two or more units of work or groups of bid items, identified separately in the Bid Proposal, from which the Contracting Agency may make a choice between different methods or material of construction for performing the same work.

Business Day

A business day is any day from Monday through Friday except holidays as listed in Section 1-08.5.

Contract Bond

The definition in the Standard Specifications for “Contract Bond” applies to whatever bond form(s) are required by the Contract Documents, which may be a combination of a Payment Bond and a Performance Bond.

Contract Documents

See definition for “Contract”.

Contract Time

The period of time established by the terms and conditions of the Contract within which the Work must be physically completed.

Notice of Award

The written notice from the Contracting Agency to the successful Bidder signifying the Contracting Agency’s acceptance of the Bid Proposal.

Notice to Proceed

The written notice from the Contracting Agency or Engineer to the Contractor authorizing and directing the Contractor to proceed with the Work and establishing the date on which the Contract time begins.

Traffic

Both vehicular and non-vehicular traffic, such as pedestrians, bicyclists, wheelchairs, and equestrian traffic.

1-02 BID PROCEDURES AND CONDITIONS

1-02.1 Prequalification of Bidders

Delete this Section and replace it with the following:

1-02.1 Qualifications of Bidder

(January 24, 2011 APWA GSP)

Before award of a public works contract, a bidder must meet at least the minimum qualifications of RCW 39.04.350(1) to be considered a responsible bidder and qualified to be awarded a public works project.

1-02.1(1) Supplemental Qualifications Criteria

(July 31, 2017 APWA GSP)

In addition, the Contracting Agency has established Contracting Agency-specific and/or project-specific supplemental criteria, in accordance with RCW 39.04.350(3), for determining Bidder responsibility, including the basis for evaluation and the deadline for appealing a determination that a Bidder is not responsible. These criteria are contained in Section 1-02.14 Option C of these Special Provisions.

1-02.2 Plans and Specifications

(June 27, 2011 APWA GSP)

Delete this section and replace it with the following:

Information as to where Bid Documents can be obtained or reviewed will be found in the Call for Bids (Advertisement for Bids) for the work.

After award of the contract, plans and specifications will be issued to the Contractor at no cost as detailed below:

To Prime Contractor	No. of Sets	Basis of Distribution
Reduced plans (11" x 17")	3	Furnished only upon request
Contract Provisions	3	Furnished only upon request
Large plans (22" x 34")	3	Furnished only upon request

Additional plans and Contract Provisions may be obtained by the Contractor from the source stated in the Call for Bids, at the Contractor's own expense.

1-02.4 Examination of Plans, Specifications and Site of Work

1-02.4(1) General

(December 30, 2022 APWA GSP Option A)

The first sentence of the ninth paragraph, beginning with "Prospective Bidder desiring...", is revised to read:

Prospective Bidder desiring an explanation or interpretation of the Bid Documents, shall request the explanation or interpretation in writing soon enough to allow a written reply to reach all prospective Bidders before the submission of their Bids.

1-02.5 Proposal Forms

(July 31, 2017 APWA GSP)

Delete this section and replace it with the following:

The Proposal Form will identify the project and its location and describe the work. It will also list estimated quantities, units of measurement, the items of work, and the materials to be furnished at the unit bid prices. The bidder shall complete spaces on the proposal form that call for, but are not limited to, unit prices; extensions; summations; the total bid amount; signatures; date; and, where applicable, retail sales taxes and acknowledgment of addenda; the bidder's name, address, telephone number, and signature; the bidder's UDBE/DBE/M/WBE commitment, if applicable; a State of Washington Contractor's Registration Number; and a Business License Number, if applicable. Bids shall be completed by typing or shall be printed in ink by hand, preferably in black ink. The required certifications are included as part of the Proposal Form.

The Contracting Agency reserves the right to arrange the proposal forms with alternates and additives, if such be to the advantage of the Contracting Agency. The bidder shall bid on all alternates and additives set forth in the Proposal Form unless otherwise specified.

1-02.6 Preparation of Proposal

(March 3, 2022 Lacey GSP)

Supplement the second paragraph with the following:

4. If a minimum bid amount has been established for any item, the unit or lump sum price must equal or exceed the minimum amount stated.

5. Any correction to a bid made by interlineation, alteration, or erasure, shall be initialed by the signer of the bid.

Delete the last two paragraphs, and replace it with the following:

The Bidder shall submit a completed Contractor Certification Wage Law Compliance form, provided by the Contracting Agency. Failure to return this certification within 24 hours of the bid opening will make this Bid Nonresponsive and ineligible for Award. A Contractor Certification of Wage Law Compliance form is included in the Proposal Forms.

The Bidder shall make no stipulation on the Bid Form, nor qualify the bid in any manner.

A bid by a corporation shall be executed in the corporate name, by the president or a vice president (or other corporate officer accompanied by evidence of authority to sign).

A bid by a partnership shall be executed in the partnership name, and signed by a partner.

A bid by a joint venture shall be executed in the joint venture name and signed by a member of the joint venture.

1-02.6 Preparation of Proposal

[\(August 2, 2004 WSDOT 1-02.6OPT15.GR1\)](#)

The fifth and sixth paragraphs of Section 1-02.6 are deleted.

1-02.7 Bid Deposit

[\(March 8, 2013 APWA GSP\)](#)

Supplement this section with the following:

Bid bonds shall contain the following:

1. Contracting Agency-assigned number for the project;
2. Name of the project;
3. The Contracting Agency named as obligee;
4. The amount of the bid bond stated either as a dollar figure or as a percentage which represents five percent of the maximum bid amount that could be awarded;
5. Signature of the bidder's officer empowered to sign official statements. The signature of the person authorized to submit the bid should agree with the signature on the bond, and the title of the person must accompany the said signature;
6. The signature of the surety's officer empowered to sign the bond and the power of attorney.

If so stated in the Contract Provisions, bidder must use the bond form included in the Contract Provisions.

If so stated in the Contract Provisions, cash will not be accepted for a bid deposit.

1-02.9 Delivery of Proposal

[\(March 3, 2022 Lacey GSP\)](#)

Delete this section and replace it with the following:

Each Proposal shall be submitted in a sealed envelope, with the Project Name and Project Number as stated in the Call for Bids clearly marked on the outside of the envelope, or as otherwise required in the Bid Documents, to ensure proper handling and delivery.

If supplemental information is due after the Bid Proposal is due, the document(s) shall be submitted as follows:

1. In a sealed envelope labeled the same as for the Proposal, with “Supplemental Information” added, or
2. By e-mail to the following e-mail address: ProjectAdmin@ci.lacey.wa.us

All other information required to be submitted with the Bid Proposal must be submitted with the Bid Proposal itself, at the time stated in the Call for Bids.

Proposals that are received as required will be publicly opened and read as specified in Section 1-02.12. The Contracting Agency will not open or consider any Bid Proposal that is received after the time specified in the Call for Bids for receipt of Bid Proposals, or received in a location other than that specified in the Call for Bids. The Contracting Agency will not open or consider any “Supplemental Information” that is received after the time specified, or received in a location other than that specified in the Call for Bids.

If an emergency or unanticipated event interrupts normal work processes of the Contracting Agency so that Proposals cannot be received at the office designated for receipt of bids as specified in Section 1-02.12 the time specified for receipt of the Proposal will be deemed to be extended to the same time of day specified in the solicitation on the first work day on which the normal work processes of the Contracting Agency resume.

1-02.10 Withdrawing, Revising, or Supplementing Proposal **(July 23, 2015 APWA GSP)**

Delete this section in its entirety, and replace it with the following:

After submitting a physical Bid Proposal to the Contracting Agency, the Bidder may withdraw, revise, or supplement it if:

1. The Bidder submits a written request signed by an authorized person and physically delivers it to the place designated for receipt of Bid Proposals, and
2. The Contracting Agency receives the request before the time set for receipt of Bid Proposals, and
3. The revised or supplemented Bid Proposal (if any) is received by the Contracting Agency before the time set for receipt of Bid Proposals.

If the Bidder’s request to withdraw, revise, or supplement its Bid Proposal is received before the time set for receipt of Bid Proposals, the Contracting Agency will return the unopened Proposal package to the Bidder. The Bidder must then submit the revised or supplemented package in its entirety. If the Bidder does not submit a revised or supplemented package, then its bid shall be considered withdrawn.

Late revised or supplemented Bid Proposals or late withdrawal requests will be date recorded by the Contracting Agency and returned unopened. Mailed, Emailed, or faxed requests to withdraw, revise, or supplement a Bid Proposal are not acceptable.

1-02.12 Public Opening of Proposals **(November 20, 2020 Lacey GSP)**

Delete and replace this section with the following:

Proposals will be opened and publicly read by live video stream per the “Instructions to Bidders” in Section A of these Specifications at the time as indicated in the call for Bids

1-02.13 Irregular Proposals
(December 30, 2022 APWA GSP)

Delete this section and replace it with the following:

1. A Proposal will be considered irregular and will be rejected if:
 - a. The Bidder is not prequalified when so required;
 - b. The authorized Proposal form furnished by the Contracting Agency is not used or is altered;
 - c. The completed Proposal form contains any unauthorized additions, deletions, alternate Bids, or conditions;
 - d. The Bidder adds provisions reserving the right to reject or accept the award, or enter into the Contract;
 - e. A price per unit cannot be determined from the Bid Proposal;
 - f. The Proposal form is not properly executed;
 - g. The Bidder fails to submit or properly complete a Subcontractor list (WSDOT Form 271-015), if applicable, as required in Section 1-02.6;
 - h. The Bidder fails to submit or properly complete a Disadvantaged Business Enterprise Certification (WSDOT Form 272-056), if applicable, as required in Section 1-02.6;
 - i. The Bidder fails to submit Written Confirmation (WSDOT Form 422-031) from each DBE firm listed on the Bidder’s completed DBE Utilization Certification that they are in agreement with the bidder’s DBE participation commitment, if applicable, as required in Section 1-02.6, or if the written confirmation that is submitted fails to meet the requirements of the Special Provision;
 - j. The Bidder fails to submit DBE Good Faith Effort documentation, if applicable, as required in Section 1-02.6, or if the documentation that is submitted fails to demonstrate that a Good Faith Effort to meet the Condition of Award was made;
 - k. The Bidder fails to submit a DBE Bid Item Breakdown (WSDOT Form 272-054), if applicable, as required in Section 1-02.6, or if the documentation that is submitted fails to meet the requirements of the Special Provisions;
 - l. The Bidder fails to submit DBE Trucking Credit Forms (WSDOT Form 272-058), if applicable, as required in Section 1-02.6, or if the documentation that is submitted fails to meet the requirements of the Special Provisions;
 - m. The Bid Proposal does not constitute a definite and unqualified offer to meet the material terms of the Bid invitation; or
 - n. More than one Proposal is submitted for the same project from a Bidder under the same or different names.
2. A Proposal may be considered irregular and may be rejected if:
 - a. The Proposal does not include a unit price for every Bid item;
 - b. Any of the unit prices are excessively unbalanced (either above or below the amount of a reasonable Bid) to the potential detriment of the Contracting Agency;
 - c. Receipt of Addenda is not acknowledged;
 - d. A member of a joint venture or partnership and the joint venture or partnership submit Proposals for the same project (in such an instance, both Bids may be rejected); or
 - e. If Proposal form entries are not made in ink.

1-02.14 Disqualification of Bidders
(May 17, 2018 APWA GSP Option A)

Delete this Section and replace it with the following:

A Bidder will be deemed not responsible if the Bidder does not meet the mandatory bidder responsibility criteria in RCW 39.04.350(1), as amended.

The Contracting Agency will verify that the Bidder meets the mandatory bidder responsibility criteria in RCW 39.04.350(1). To assess bidder responsibility, the Contracting Agency reserves the right to request documentation as needed from the Bidder and third parties concerning the Bidder's compliance with the mandatory bidder responsibility criteria.

If the Contracting Agency determines the Bidder does not meet the mandatory bidder responsibility criteria in RCW 39.04.350(1) and is therefore not a responsible Bidder, the Contracting Agency shall notify the Bidder in writing, with the reasons for its determination. If the Bidder disagrees with this determination, it may appeal the determination within two (2) business days of the Contracting Agency's determination by presenting its appeal and any additional information to the Contracting Agency. The Contracting Agency will consider the appeal and any additional information before issuing its final determination. If the final determination affirms that the Bidder is not responsible, the Contracting Agency will not execute a contract with any other Bidder until at least two business days after the Bidder determined to be not responsible has received the Contracting Agency's final determination..

1-02.15 Pre-Award Information **(August 14, 2013 APWA GSP)**

Revise this section to read:

Before awarding any contract, the Contracting Agency may require one or more of these items or actions of the apparent lowest responsible bidder:

1. A complete statement of the origin, composition, and manufacture of any or all materials to be used,
2. Samples of these materials for quality and fitness tests,
3. A progress schedule (in a form the Contracting Agency requires) showing the order of and time required for the various phases of the work,
4. A breakdown of costs assigned to any bid item,
5. Attendance at a conference with the Engineer or representatives of the Engineer,
6. Obtain, and furnish a copy of, a business license to do business in the city or county where the work is located.
7. Any other information or action taken that is deemed necessary to ensure that the bidder is the lowest responsible bidder.

1-03 AWARD AND EXECUTION OF CONTRACT

1-03.1 Consideration of Bids **(December 30, 2022 APWA GSP)**

Revise the first paragraph to read:

After opening and reading proposals, the Contracting Agency will check them for correctness of extensions of the prices per unit and the total price. If a discrepancy exists between the price per unit and the extended amount of any bid item, the price per unit will control. If a minimum bid amount has been established for any item and the bidder's unit or lump sum price is less than the minimum specified amount, the Contracting Agency will unilaterally revise the unit or lump sum price, to the minimum specified amount and recalculate the extension. The total of extensions, corrected where necessary, including sales taxes where applicable and such additives and/or alternates as selected by the Contracting

Agency, will be used by the Contracting Agency for award purposes and to fix the Awarded Contract Price amount and the amount of the contract bond.

1-03.3 Execution of Contract

(January 19, 2022 APWA GSP)

Revise this section to read:

Within 3 calendar days of Award date (not including Saturdays, Sundays and Holidays), the successful Bidder shall provide the information necessary to execute the Contract to the Contracting Agency. The Bidder shall send the contact information, including the full name, email address, and phone number, for the authorized signer and bonding agent to the Contracting Agency.

Copies of the Contract Provisions, including the unsigned Form of Contract, will be available for signature by the successful bidder on the first business day following award. The number of copies to be executed by the Contractor will be determined by the Contracting Agency.

Within 10 calendar days after the award date, the successful bidder shall return the signed Contracting Agency-prepared contract, an insurance certification as required by Section 1-07.18, a satisfactory bond as required by law and Section 1-03.4, and the Transfer of Coverage form for the Construction Stormwater General Permit with sections I, III, and VIII completed when provided. Before execution of the contract by the Contracting Agency, the successful bidder shall provide any pre-award information the Contracting Agency may require under Section 1-02.15.

Until the Contracting Agency executes a contract, no proposal shall bind the Contracting Agency nor shall any work begin within the project limits or within Contracting Agency-furnished sites. The Contractor shall bear all risks for any work begun outside such areas and for any materials ordered before the contract is executed by the Contracting Agency.

If the bidder experiences circumstances beyond their control that prevents return of the contract documents within the calendar days after the award date stated above, the Contracting Agency may grant up to a maximum of 10 additional calendar days for return of the documents, provided the Contracting Agency deems the circumstances warrant it.

1-03.4 Contract Bond

(July 23, 2015 APWA GSP)

Delete the first paragraph and replace it with the following:

The successful bidder shall provide executed payment and performance bond(s) for the full contract amount. The bond may be a combined payment and performance bond; or be separate payment and performance bonds. In the case of separate payment and performance bonds, each shall be for the full contract amount. The bond(s) shall:

1. Be on Contracting Agency-furnished form(s);
2. Be signed by an approved surety (or sureties) that:
 - a) Is registered with the Washington State Insurance Commissioner, and
 - b) Appears on the current Authorized Insurance List in the State of Washington published by the Office of the Insurance Commissioner,
3. Guarantee that the Contractor will perform and comply with all obligations, duties, and conditions under the Contract, including but not limited to the duty and obligation to indemnify, defend, and protect the Contracting Agency against all losses and claims related directly or indirectly from any failure:

- a) Of the Contractor (or any of the employees, subcontractors, or lower tier subcontractors of the Contractor) to faithfully perform and comply with all contract obligations, conditions, and duties, or
- b) Of the Contractor (or the subcontractors or lower tier subcontractors of the Contractor) to pay all laborers, mechanics, subcontractors, lower tier subcontractors, material person, or any other person who provides supplies or provisions for carrying out the work;
- 4. Be conditioned upon the payment of taxes, increases, and penalties incurred on the project under titles 50, 51, and 82 RCW; and
- 5. Be accompanied by a power of attorney for the Surety's officer empowered to sign the bond; and
- 6. Be signed by an officer of the Contractor empowered to sign official statements (sole proprietor or partner). If the Contractor is a corporation, the bond(s) must be signed by the president or vice president, unless accompanied by written proof of the authority of the individual signing the bond(s) to bind the corporation (i.e., corporate resolution, power of attorney, or a letter to such effect signed by the president or vice president).

1-03.4(1) Retainage in Lieu of Contract Bond
(May 17, 2018 APWA GSP)

Add the following new section:

For contracts of \$150,000 or less, the Contractor may, at the Contractor's option, authorize the Contracting Agency to retain 10% of the contract amount in lieu of furnishing a performance and/or payment bond. If the Contractor elects this option, the retainage shall be held for a period of thirty (30) days after the date of final acceptance, or until receipt of all necessary releases from the Departments of Revenue and of Labor and Industries and settlement of any liens filed under RCW 60.28, whichever is later. The Contractor must advise the Contracting Agency in writing of the Contractor's election to authorize retainage in lieu of a bond, at the time of execution of the Contract.

In choosing this option, the Contractor agrees that if the Contractor, its heirs, executors, administrators, successors, or assigns, shall in all things stand to and abide by, and well and truly keep and perform the covenants, conditions and agreements in the Contract, and shall faithfully perform all the provisions of such contract and shall also well and truly perform and fulfill all the undertakings, covenants, terms, conditions and agreements of any and all duly authorized modifications of the Contract that may hereafter be made, at the time and in the manner therein specified, and shall pay all laborers, mechanics, subcontractors, and material suppliers, and all persons who shall supply such person or persons, or subcontractors, with provisions and supplies for the carrying on of such work, on his or her part, and shall indemnify and save harmless the Contracting Agency, its officers and agents from any claim for such payment, then the funds retained in lieu of a performance bond shall be released at the time provided above; otherwise, the funds shall be retained until the Contractor fulfills the said obligations.

1-03.7 Judicial Review
(December 30, 2022 APWA GSP)

Revise this section to read:

All decisions made by the Contracting Agency regarding the Award and execution of the Contract or Bid rejection shall be conclusive subject to the scope of judicial review permitted under Washington Law. Such review, if any, shall be timely filed in the Superior Court of the county where the Contracting Agency headquarters is located, provided that where an action is asserted against a county, RCW 36.01.050 shall control venue and jurisdiction.

1-04 SCOPE OF THE WORK

1-04.2 Coordination of Contract Documents, Plans, Special Provisions, Specifications, and Addenda

(December 30, 2022 APWA GSP)

Revise the second paragraph to read:

Any inconsistency in the parts of the contract shall be resolved by following this order of precedence (e.g., 1 presiding over 2, 2 presiding over 3, 3 over 4, and so forth):

1. Addenda,
2. Proposal Form,
3. Special Provisions,
4. Contract Plans,
5. Standard Specifications,
6. City of Lacey Development Guidelines and Public Works Standards, and
7. WSDOT Standard Plans for Road, Bridge and Municipal Construction

1-04.2 Coordination of Contract Documents, Plans, Special Provisions, Specifications, and Addenda

(November 20, 2020 Lacey GSP)

Revise the second paragraph to read:

Any inconsistency in the parts of the contract shall be resolved by following this order of precedence (e.g., 1 presiding over 2, 2 presiding over 3, 3 over 4, and so forth):

1. Contract Form,
2. Addenda (if any),
3. Proposal Form,
4. Special Provisions,
5. Technical Specifications, if included,
6. Contract Plans,
7. WSDOT Standard Specifications for Road, Bridge, and Municipal Construction,
8. City of Lacey Development Guidelines and Public Works Standards, and
9. WSDOT Standard Plans for Road, Bridge and Municipal Construction

1-04.4(1) Minor Changes

(May 30, 2019 APWA GSP)

Delete the first paragraph and replace it with the following:

Payments or credits for changes amounting to \$15,000 or less may be made under the Bid item “Minor Change”. At the discretion of the Contracting Agency, this procedure for Minor Changes may be used in lieu of the more formal procedure as outlined in Section 1-04.4, Changes. All “Minor Change” work will be within the scope of the Contract Work and will not change Contract Time.

1-04.5 Procedure, Protest, and Dispute by the Contractor

(January 19, 2022 APWA GSP)

Revise item 1 of the first paragraph to read:

1. Give a signed written notice of protest to the Engineer or the Engineer's field Inspectors within 5 calendar days of receiving a change order or an Engineer's Written Determination.

1-04.6 Variations in Estimated Quantities

(December 30, 2022 APWA GSP Option B)

Revise the first paragraph to read:

Payment to the Contractor will be made only for the actual quantities of Work performed and accepted in conformance with the Contract. When the accepted quantity of Work performed under a unit item varies from the original Proposal quantity, payment will be at the unit Contract price for all Work unless the total accepted quantity of the Contract item, adjusted to exclude added or deleted amounts included in change orders accepted by both parties, increases or decreases by more than 25 percent from the original Proposal quantity, and if the total extended bid price for that item at time of award is equal to or greater than 10 percent of the total contract price at time of award. In that case, payment for contract work may be adjusted as described herein.

1-05 CONTROL OF WORK

Roadway and Utility Surveys

(July 23, 2015 APWA GSP, Option 1)

The Engineer shall furnish to the Contractor one time only all principal lines, grades, and measurements the Engineer deems necessary for completion of the work. These shall generally consist of one initial set of:

1. Slope stakes for establishing grading;
2. Curb grade stakes;
3. Centerline finish grade stakes for pavement sections wider than 25 feet; and
4. Offset points to establish line and grade for underground utilities such as water, sewers, and storm drains.

On alley construction projects with minor grade changes, the Engineer shall provide only offset hubs on one side of the alley to establish the alignment and grade.

1-05.4(2) Survey Control and Electronic Files

(August 10, 2010 Lacey GSP)

Add the following new section:

The Contractor shall re-establish the survey control used in design by using existing survey monuments and other control points as provided by the City.

When requested by the Contractor, the City will provide an electronic version of the construction plans (drawings), for use by the Contractor at the Contractor's own risk. In all cases, the approved paper construction plans are the official contract documents. If the Contractor wishes to use the electronic version of the construction plans for the purposes of providing surveying of the proposed improvements, it shall be the Contractor's responsibility to verify that any coordinates used from the electronic file match the station and offset location given in the contract construction plans. Construction plans are diagrammatic in nature. The coordinate locations of the various graphic elements within the electronic files may not necessarily be precisely shown with respect to their coordinate position. In all cases, the location callouts in the contract construction plans shall govern.

1-05.7 Removal of Defective and Unauthorized Work **(October 1, 2005 APWA GSP)**

Supplement this section with the following:

If the Contractor fails to remedy defective or unauthorized work within the time specified in a written notice from the Engineer, or fails to perform any part of the work required by the Contract Documents, the Engineer may correct and remedy such work as may be identified in the written notice, with Contracting Agency forces or by such other means as the Contracting Agency may deem necessary.

If the Contractor fails to comply with a written order to remedy what the Engineer determines to be an emergency situation, the Engineer may have the defective and unauthorized work corrected immediately, have the rejected work removed and replaced, or have work the Contractor refuses to perform completed by using Contracting Agency or other forces. An emergency situation is any situation when, in the opinion of the Engineer, a delay in its remedy could be potentially unsafe, or might cause serious risk of loss or damage to the public.

Direct or indirect costs incurred by the Contracting Agency attributable to correcting and remedying defective or unauthorized work, or work the Contractor failed or refused to perform, shall be paid by the Contractor. Payment will be deducted by the Engineer from monies due, or to become due, the Contractor. Such direct and indirect costs shall include in particular, but without limitation, compensation for additional professional services required, and costs for repair and replacement of work of others destroyed or damaged by correction, removal, or replacement of the Contractor's unauthorized work.

No adjustment in contract time or compensation will be allowed because of the delay in the performance of the work attributable to the exercise of the Contracting Agency's rights provided by this Section.

The rights exercised under the provisions of this section shall not diminish the Contracting Agency's right to pursue any other avenue for additional remedy or damages with respect to the Contractor's failure to perform the work as required.

1-05.11 Final Inspections and Operational Testing **(October 1, 2005 APWA GSP)**

Delete this section and replace it with the following:

1-05.11(1) Substantial Completion Date

When the Contractor considers the work to be substantially complete, the Contractor shall so notify the Engineer and request the Engineer establish the Substantial Completion Date. The Contractor's request shall list the specific items of work that remain to be completed in order to reach physical completion. The Engineer will schedule an inspection of the work with the Contractor to determine the status of completion. The Engineer may also establish the Substantial Completion Date unilaterally.

If, after this inspection, the Engineer concurs with the Contractor that the work is substantially complete and ready for its intended use, the Engineer, by written notice to the Contractor, will set the Substantial Completion Date. If, after this inspection the Engineer does not consider the work substantially complete and ready for its intended use, the Engineer will, by written notice, so notify the Contractor giving the reasons therefore.

Upon receipt of written notice concurring in or denying substantial completion, whichever is applicable, the Contractor shall pursue vigorously, diligently and without unauthorized interruption, the work necessary to reach Substantial and Physical Completion. The Contractor shall provide the Engineer with a

revised schedule indicating when the Contractor expects to reach substantial and physical completion of the work.

The above process shall be repeated until the Engineer establishes the Substantial Completion Date and the Contractor considers the work physically complete and ready for final inspection.

1-05.11(2) Final Inspection and Physical Completion Date

When the Contractor considers the work physically complete and ready for final inspection, the Contractor by written notice, shall request the Engineer to schedule a final inspection. The Engineer will set a date for final inspection. The Engineer and the Contractor will then make a final inspection and the Engineer will notify the Contractor in writing of all particulars in which the final inspection reveals the work incomplete or unacceptable. The Contractor shall immediately take such corrective measures as are necessary to remedy the listed deficiencies. Corrective work shall be pursued vigorously, diligently, and without interruption until physical completion of the listed deficiencies. This process will continue until the Engineer is satisfied the listed deficiencies have been corrected.

If action to correct the listed deficiencies is not initiated within 7 days after receipt of the written notice listing the deficiencies, the Engineer may, upon written notice to the Contractor, take whatever steps are necessary to correct those deficiencies pursuant to Section 1-05.7.

The Contractor will not be allowed an extension of contract time because of a delay in the performance of the work attributable to the exercise of the Engineer's right hereunder.

Upon correction of all deficiencies, the Engineer will notify the Contractor and the Contracting Agency, in writing, of the date upon which the work was considered physically complete. That date shall constitute the Physical Completion Date of the contract, but shall not imply acceptance of the work or that all the obligations of the Contractor under the contract have been fulfilled.

1-05.11(3) Operational Testing

It is the intent of the Contracting Agency to have at the Physical Completion Date a complete and operable system. Therefore when the work involves the installation of machinery or other mechanical equipment; street lighting, electrical distribution or signal systems; irrigation systems; buildings; or other similar work it may be desirable for the Engineer to have the Contractor operate and test the work for a period of time after final inspection but prior to the physical completion date. Whenever items of work are listed in the Contract Provisions for operational testing they shall be fully tested under operating conditions for the time period specified to ensure their acceptability prior to the Physical Completion Date. During and following the test period, the Contractor shall correct any items of workmanship, materials, or equipment which prove faulty, or that are not in first class operating condition. Equipment, electrical controls, meters, or other devices and equipment to be tested during this period shall be tested under the observation of the Engineer, so that the Engineer may determine their suitability for the purpose for which they were installed. The Physical Completion Date cannot be established until testing and corrections have been completed to the satisfaction of the Engineer.

The costs for power, gas, labor, material, supplies, and everything else needed to successfully complete operational testing, shall be included in the unit contract prices related to the system being tested, unless specifically set forth otherwise in the proposal.

Operational and test periods, when required by the Engineer, shall not affect a manufacturer's guaranties or warranties furnished under the terms of the contract.

1-05.12(1) One-Year Guarantee Period
(March 8, 2013 APWA GSP)

Add the following new section:

The Contractor shall return to the project and repair or replace all defects in workmanship and material discovered within one year after Final Acceptance of the Work. The Contractor shall start work to remedy any such defects within 7 calendar days of receiving Contracting Agency's written notice of a defect, and shall complete such work within the time stated in the Contracting Agency's notice. In case of an emergency, where damage may result from delay or where loss of services may result, such corrections may be made by the Contracting Agency's own forces or another contractor, in which case the cost of corrections shall be paid by the Contractor. In the event the Contractor does not accomplish corrections within the time specified, the work will be otherwise accomplished and the cost of same shall be paid by the Contractor.

When corrections of defects are made, the Contractor shall then be responsible for correcting all defects in workmanship and materials in the corrected work for one year after acceptance of the corrections by Contracting Agency.

This guarantee is supplemental to and does not limit or affect the requirements that the Contractor's work comply with the requirements of the Contract or any other legal rights or remedies of the Contracting Agency.

1-05.15 Method of Serving Notices
(December 30, 2022 APWA GSP)

Revise the second paragraph to read:

All correspondence from the Contractor shall be directed to the Project Engineer. All correspondence from the Contractor constituting any notification, notice of protest, notice of dispute, or other correspondence constituting notification required to be furnished under the Contract, must be in paper format, hand delivered or sent via mail delivery service to the Project Engineer's office. Electronic copies such as e-mails or electronically delivered copies of correspondence will not constitute such notice and will not comply with the requirements of the Contract.

1-05.16 Water and Power
(October 1, 2005 APWA GSP)

Add the following new section:

The Contractor shall make necessary arrangements, and shall bear the costs for power and water necessary for the performance of the work, unless the contract includes power and water as a pay item.

1-05.18 Record Drawings
(January 3, 2011 Lacey GSP Option A)

Add the following new section:

The Contractor shall furnish As-Built/Record Drawings of all changes to the original plans in accordance with the following conditions:

One set of 22"x 34" plans showing the changes to the project as installed.
Drawings shall be to scale with all notations neat in appearance.

Turn the record drawings over to the Engineer for review and approval prior to final payment.

1-06 CONTROL OF MATERIAL

1-06.1 Approval of Materials Prior to Use

(January 4, 2016 Lacey GSP)

The second sentence of first paragraph is revised to read:

The Contractor shall use the Qualified Product List (QPL), the Aggregate Source Approval (ASA) Database, or the City of Lacey Request for Approval of Material (COL RAM) form.

1-06.1(2) Request for Approval of Material (RAM)

The first paragraph is revised to read:

The COL RAM shall be used with all submittals. The COL RAM shall be prepared by the Contractor in accordance with the instructions and submitted to the engineer for approval before the material is incorporated into the Work..

Supplement this section with the following:

The Contractor shall submit sufficient information that describes the materials proposed as defined and described in these specifications and plans within 10 working days following the Notice to Proceed.

The City of Lacey has identified the following items as long lead items.

1. Kennel components (bases, side panels, back panels, doors, etc.)

Long lead items shall be submitted within 10 working days of Notice to Proceed. The list above may not include all long lead items. The contractor is responsible for identifying all items and shall notify the Engineer of any additional items.

The Contractor shall submit one electronic of catalog cuts, shop drawings, and a material testing sample, as required for all items to be used in this contract for approval. The Contractor shall circle or highlight products and materials that are specific to this project, and cross out items that are not for this project.

All items not in exact compliance with the specifications must be noted as a change. The Contractor shall include an explanation, product specifications, sample articles, and any other items that will aid the Engineer in approving an item not in exact accordance with the specifications.

All submittals shall be submitted in Adobe Acrobat format and submittals that exceed 10 pages shall include a table of contents. Submittals that are not submitted in the format outlined may be rejected outright and the Contractor is required to resubmit in the correct format. The form and the submittal shall be sent in the same e-mail. Submittals that exceed 10 MB shall either be provided on a CD, a flash drive or via an internet link.

The Engineer will review submittals within 10 working days. The Contractor may request additional working days if approval or disapproval is not received in 10 working days. The Contractor may not request additional working days for failure to submit sufficient information to approve an item, or for rejection of an item not in accordance with the specifications.

Resubmittals shall be submitted within 5 working days from City's transmittal, to the contractor, of the Engineer reviewed submittal. If the submittal is "Rejected", the contractor shall resubmit the entire

submittal. If the submittal is marked “Revise and Resubmit”, the contractor shall submit items that are identified in the Engineer’s comments.

Any material purchased or labor performed prior to such approval shall be at the Contractor's risk. The Contractor must receive all material approvals before the materials will be allowed on the project.

1-07 LEGAL RELATIONS AND RESPONSIBILITIES TO THE PUBLIC

1-07.1 Laws to be Observed

(October 1, 2005 APWA GSP)

Supplement this section with the following:

In cases of conflict between different safety regulations, the more stringent regulation shall apply.

The Washington State Department of Labor and Industries shall be the sole and paramount administrative agency responsible for the administration of the provisions of the Washington Industrial Safety and Health Act of 1973 (WISHA).

The Contractor shall maintain at the project site office, or other well-known place at the project site, all articles necessary for providing first aid to the injured. The Contractor shall establish, publish, and make known to all employees, procedures for ensuring immediate removal to a hospital, or doctor’s care, persons, including employees, who may have been injured on the project site. Employees should not be permitted to work on the project site before the Contractor has established and made known procedures for removal of injured persons to a hospital or a doctor’s care.

The Contractor shall have sole responsibility for the safety, efficiency, and adequacy of the Contractor’s plant, appliances, and methods, and for any damage or injury resulting from their failure, or improper maintenance, use, or operation. The Contractor shall be solely and completely responsible for the conditions of the project site, including safety for all persons and property in the performance of the work. This requirement shall apply continuously, and not be limited to normal working hours. The required or implied duty of the Engineer to conduct construction review of the Contractor’s performance does not, and shall not, be intended to include review and adequacy of the Contractor’s safety measures in, on, or near the project site.

1-07.2 State Sales Tax

(June 27, 2011 APWA GSP)

Delete this section, including its sub-sections, in its entirety and replace it with the following:

The Washington State Department of Revenue has issued special rules on the State sales tax. Sections 1-07.2(1) through 1-07.2(3) are meant to clarify those rules. The Contractor should contact the Washington State Department of Revenue for answers to questions in this area. The Contracting Agency will not adjust its payment if the Contractor bases a bid on a misunderstood tax liability.

The Contractor shall include all Contractor-paid taxes in the unit bid prices or other contract amounts. In some cases, however, state retail sales tax will not be included. Section 1-07.2(2) describes this exception.

The Contracting Agency will pay the retained percentage (or release the Contract Bond if a FHWA-funded Project) only if the Contractor has obtained from the Washington State Department of Revenue a certificate showing that all contract-related taxes have been paid (RCW 60.28.051). The Contracting Agency may deduct from its payments to the Contractor any amount the Contractor may owe the

Washington State Department of Revenue, whether the amount owed relates to this contract or not. Any amount so deducted will be paid into the proper State fund.

1-07.2(1) State Sales Tax — Rule 171

WAC 458-20-171, and its related rules, apply to building, repairing, or improving streets, roads, etc., which are owned by a municipal corporation, or political subdivision of the state, or by the United States, and which are used primarily for foot or vehicular traffic. This includes storm or combined sewer systems within and included as a part of the street or road drainage system and power lines when such are part of the roadway lighting system. For work performed in such cases, the Contractor shall include Washington State Retail Sales Taxes in the various unit bid item prices, or other contract amounts, including those that the Contractor pays on the purchase of the materials, equipment, or supplies used or consumed in doing the work.

1-07.2(2) State Sales Tax — Rule 170

WAC 458-20-170, and its related rules, apply to the constructing and repairing of new or existing buildings, or other structures, upon real property. This includes, but is not limited to, the construction of streets, roads, highways, etc., owned by the state of Washington; water mains and their appurtenances; sanitary sewers and sewage disposal systems unless such sewers and disposal systems are within, and a part of, a street or road drainage system; telephone, telegraph, electrical power distribution lines, or other conduits or lines in or above streets or roads, unless such power lines become a part of a street or road lighting system; and installing or attaching of any article of tangible personal property in or to real property, whether or not such personal property becomes a part of the realty by virtue of installation.

For work performed in such cases, the Contractor shall collect from the Contracting Agency, retail sales tax on the full contract price. The Contracting Agency will automatically add this sales tax to each payment to the Contractor. For this reason, the Contractor shall not include the retail sales tax in the unit bid item prices, or in any other contract amount subject to Rule 170, with the following exception.

Exception: The Contracting Agency will not add in sales tax for a payment the Contractor or a subcontractor makes on the purchase or rental of tools, machinery, equipment, or consumable supplies not integrated into the project. Such sales taxes shall be included in the unit bid item prices or in any other contract amount.

1-07.2(3) Services

The Contractor shall not collect retail sales tax from the Contracting Agency on any contract wholly for professional or other services (as defined in Washington State Department of Revenue Rules 138 and 244).

1-07.6 Permits and Licenses

(February 14, 2023 Lacey GSP)

Section 1-07.6 is supplemented with the following:

The Contractor shall be responsible for obtaining the permits listed below. The Contractor shall obtain any additional permits as necessary. All costs to obtain and comply with permits shall be included in the applicable Bid items for the Work involved.

NAME OF DOCUMENT	PERMITTING AGENCY
Building/Miscellaneous	City of Olympia
Plumbing	City of Olympia

1-07.18 Public Liability and Property Damage Insurance

Delete this section in its entirety, and replace it with the following:

1-07.18 Insurance

(December 30, 2022 APWA GSP)

1-07.18(1) General Requirements

A. The Contractor shall procure and maintain the insurance described in all subsections of section 1-07.18 of these Special Provisions, from insurers with a current A. M. Best rating of not less than A-: VII and licensed to do business in the State of Washington. The Contracting Agency reserves the right to approve or reject the insurance provided, based on the insurer's financial condition.

B. The Contractor shall keep this insurance in force without interruption from the commencement of the Contractor's Work through the term of the Contract and for thirty (30) days after the Physical Completion date, unless otherwise indicated below.

C. If any insurance policy is written on a claims made form, its retroactive date, and that of all subsequent renewals, shall be no later than the effective date of this Contract. The policy shall state that coverage is claims made, and state the retroactive date. Claims-made form coverage shall be maintained by the Contractor for a minimum of 36 months following the Completion Date or earlier termination of this Contract, and the Contractor shall annually provide the Contracting Agency with proof of renewal. If renewal of the claims made form of coverage becomes unavailable, or economically prohibitive, the Contractor shall purchase an extended reporting period ("tail") or execute another form of guarantee acceptable to the Contracting Agency to assure financial responsibility for liability for services performed.

D. The Contractor's Automobile Liability, Commercial General Liability and Excess or Umbrella Liability insurance policies shall be primary and non-contributory insurance as respects the Contracting Agency's insurance, self-insurance, or self-insured pool coverage. Any insurance, self-insurance, or self-insured pool coverage maintained by the Contracting Agency shall be excess of the Contractor's insurance and shall not contribute with it.

E. The Contractor shall provide the Contracting Agency and all additional insureds with written notice of any policy cancellation, within two business days of their receipt of such notice.

F. The Contractor shall not begin work under the Contract until the required insurance has been obtained and approved by the Contracting Agency

G. Failure on the part of the Contractor to maintain the insurance as required shall constitute a material breach of contract, upon which the Contracting Agency may, after giving five business days' notice to the Contractor to correct the breach, immediately terminate the Contract or, at its discretion, procure or renew

such insurance and pay any and all premiums in connection therewith, with any sums so expended to be repaid to the Contracting Agency on demand, or at the sole discretion of the Contracting Agency, offset against funds due the Contractor from the Contracting Agency.

H. All costs for insurance shall be incidental to and included in the unit or lump sum prices of the Contract and no additional payment will be made.

1-07.18(2) Additional Insured

All insurance policies, with the exception of Workers Compensation, and of Professional Liability and Builder's Risk (if required by this Contract) shall name the following listed entities as additional insured(s) using the forms or endorsements required herein:

- The Contracting Agency and its officers, elected officials, employees, agents, and volunteers
- Joint Animal Services and its officers, elected officials, employees, agents, and volunteers

The above-listed entities shall be additional insured(s) for the full available limits of liability maintained by the Contractor, irrespective of whether such limits maintained by the Contractor are greater than those required by this Contract, and irrespective of whether the Certificate of Insurance provided by the Contractor pursuant to 1-07.18(4) describes limits lower than those maintained by the Contractor.

For Commercial General Liability insurance coverage, the required additional insured endorsements shall be at least as broad as ISO forms CG 20 10 10 01 for ongoing operations and CG 20 37 10 01 for completed operations.

1-07.18(3) Subcontractors

The Contractor shall cause each Subcontractor of every tier to provide insurance coverage that complies with all applicable requirements of the Contractor-provided insurance as set forth herein, except the Contractor shall have sole responsibility for determining the limits of coverage required to be obtained by Subcontractors.

The Contractor shall ensure that all Subcontractors of every tier add all entities listed in 1 07.18(2) as additional insureds, and provide proof of such on the policies as required by that section as detailed in 1-07.18(2) using an endorsement as least as broad as ISO CG 20 10 10 01 for ongoing operations and CG 20 37 10 01 for completed operations.

Upon request by the Contracting Agency, the Contractor shall forward to the Contracting Agency evidence of insurance and copies of the additional insured endorsements of each Subcontractor of every tier as required in 1-07.18(4) Verification of Coverage.

1-07.18(4) Verification of Coverage

The Contractor shall deliver to the Contracting Agency a Certificate(s) of Insurance and endorsements for each policy of insurance meeting the requirements set forth herein when the Contractor delivers the signed Contract for the work. Failure of Contracting Agency to demand such verification of coverage with these insurance requirements or failure of Contracting Agency to identify a deficiency from the insurance documentation provided shall not be construed as a waiver of Contractor's obligation to maintain such insurance.

Verification of coverage shall include:

1. An ACORD certificate or a form determined by the Contracting Agency to be equivalent.
2. Copies of all endorsements naming Contracting Agency and all other entities listed in 1 07.18(2) as additional insured(s), showing the policy number. The Contractor may submit a copy of any blanket additional insured clause from its policies instead of a separate endorsement.
3. Any other amendatory endorsements to show the coverage required herein.

4. A notation of coverage enhancements on the Certificate of Insurance shall not satisfy these requirements – actual endorsements must be submitted.

Upon request by the Contracting Agency, the Contractor shall forward to the Contracting Agency a full and certified copy of the insurance policy(s). If Builders Risk insurance is required on this Project, a full and certified copy of that policy is required when the Contractor delivers the signed Contract for the work.

1-07.18(5) Coverages and Limits

The insurance shall provide the minimum coverages and limits set forth below. Contractor's maintenance of insurance, its scope of coverage, and limits as required herein shall not be construed to limit the liability of the Contractor to the coverage provided by such insurance, or otherwise limit the Contracting Agency's recourse to any remedy available at law or in equity.

All deductibles and self-insured retentions must be disclosed and are subject to approval by the Contracting Agency. The cost of any claim payments falling within the deductible or self-insured retention shall be the responsibility of the Contractor. In the event an additional insured incurs a liability subject to any policy's deductibles or self-insured retention, said deductibles or self-insured retention shall be the responsibility of the Contractor.

1-07.18(5)A Commercial General Liability

Commercial General Liability insurance shall be written on coverage forms at least as broad as ISO occurrence form CG 00 01, including but not limited to liability arising from premises, operations, stop gap liability, independent contractors, products-completed operations, personal and advertising injury, and liability assumed under an insured contract. There shall be no exclusion for liability arising from explosion, collapse or underground property damage.

The Commercial General Liability insurance shall be endorsed to provide a per project general aggregate limit, using ISO form CG 25 03 05 09 or an equivalent endorsement.

Contractor shall maintain Commercial General Liability Insurance arising out of the Contractor's completed operations for at least three years following Substantial Completion of the Work.

Such policy must provide the following minimum limits:

\$1,000,000	Each Occurrence
\$2,000,000	General Aggregate
\$2,000,000	Products & Completed Operations Aggregate
\$1,000,000	Personal & Advertising Injury each offence
\$1,000,000	Stop Gap / Employers' Liability each accident

1-07.18(5)B Automobile Liability

Automobile Liability shall cover owned, non-owned, hired, and leased vehicles; and shall be written on a coverage form at least as broad as ISO form CA 00 01. If the work involves the transport of pollutants, the automobile liability policy shall include MCS 90 and CA 99 48 endorsements.

Such policy must provide the following minimum limit:

\$1,000,000	Combined single limit each accident
-------------	-------------------------------------

1-07.18(5)C Workers' Compensation

The Contractor shall comply with Workers' Compensation coverage as required by the Industrial Insurance laws of the State of Washington.

1-07.23 Public Convenience and Safety

1-08 PROSECUTION AND PROGRESS

Add the following new section:

1-08.0 Preliminary Matters **(May 25, 2006 APWA GSP)**

Add the following new section:

1-08.0(1) Preconstruction Conference **(October 10, 2008 APWA GSP)**

Prior to the Contractor beginning the work, a preconstruction conference will be held between the Contractor, the Engineer, and such other interested parties as may be invited. The purpose of the preconstruction conference will be:

- To review the initial progress schedule;
- To establish a working understanding among the various parties associated or affected by the work;
- To establish and review procedures for progress payment, notifications, approvals, submittals, etc.;
- To establish normal working hours for the work;
- To review safety standards and traffic control; and
- To discuss such other related items as may be pertinent to the work.

The Contractor shall prepare and submit at the preconstruction conference the following:

- A breakdown of all lump sum items;
- A preliminary schedule of working drawing submittals; and
- A list of material sources for approval if applicable.

1-08.0(2) Hours of Work **(December 8, 2014 APWA GSP)**

Except in the case of emergency or unless otherwise approved by the Engineer, the normal working hours for the Contract shall be any consecutive 8-hour period between 7:00 a.m. and 6:00 p.m. Monday through Friday, exclusive of a lunch break. If the Contractor desires different than the normal working hours stated above, the request must be submitted in writing prior to the preconstruction conference, subject to the provisions below. The working hours for the Contract shall be established at or prior to the preconstruction conference.

All working hours and days are also subject to local permit and ordinance conditions (such as noise ordinances).

If the Contractor wishes to deviate from the established working hours, the Contractor shall submit a written request to the Engineer for consideration. This request shall state what hours are being requested, and why. Requests shall be submitted for review no later than 5 prior to the day(s) the Contractor is requesting to change the hours.

If the Contracting Agency approves such a deviation, such approval may be subject to certain other conditions, which will be detailed in writing. For example:

1. On non-Federal aid projects, requiring the Contractor to reimburse the Contracting Agency for the costs in excess of straight-time costs for Contracting Agency representatives who worked during such times. (The Engineer may require designated representatives to be present during the work. Representatives who may be deemed necessary by the Engineer include, but are not limited to: survey crews; personnel from the Contracting Agency's material testing lab; inspectors; and other Contracting Agency employees or third party consultants when, in the opinion of the Engineer, such work necessitates their presence.)
2. Considering the work performed on Saturdays, Sundays, and holidays as working days with regard to the contract time.
3. Considering multiple work shifts as multiple working days with respect to contract time even though the multiple shifts occur in a single 24-hour period.
4. If a 4-10 work schedule is requested and approved the non working day for the week will be charged as a working day.
5. If Davis Bacon wage rates apply to this Contract, all requirements must be met and recorded properly on certified payroll

1-08.1 Subcontracting **(December 30, 2022 APWA GSP, Option A)**

Section 1-08.1 is supplemented with the following:

Prior to any subcontractor or lower tier subcontractor beginning work, the Contractor shall submit to the Engineer a certification (WSDOT Form 420-004) that a written agreement between the Contractor and the subcontractor or between the subcontractor and any lower tier subcontractor has been executed. This certification shall also guarantee that these subcontract agreements include all the documents required by the Special Provision Federal Agency Inspection.

A subcontractor or lower tier subcontractor will not be permitted to perform any work under the contract until the following documents have been completed and submitted to the Engineer:

1. Request to Sublet Work (WSDOT Form 421-012), and
2. Contractor and Subcontractor or Lower Tier Subcontractor Certification for Federal-aid Projects (WSDOT Form 420-004).

The Contractor shall submit to the Engineer a completed Monthly Retainage Report (WSDOT Form 272-065) within 15 calendar days after receipt of every monthly progress payment until every subcontractor and lower tier subcontractor's retainage has been released.

The Contractor's records pertaining to the requirements of this Special Provision shall be open to inspection or audit by representatives of the Contracting Agency during the life of the contract and for a period of not less than three years after the date of acceptance of the contract. The Contractor shall retain these records for that period. The Contractor shall also guarantee that these records of all subcontractors and lower tier subcontractors shall be available and open to similar inspection or audit for the same time period.

1-08.1(7)A Subcontracting **(December 30, 2022 APWA GSP)**

Delete the ninth paragraph, beginning with "On all projects, the Contractor shall certify..."..

1-08.3(2)A Type A Progress Schedule **(December 30, 2022 APWA GSP)**

Revise this section to read:

The Contractor shall submit five (5) copies of a Type A Progress Schedule no later than at the preconstruction conference, or some other mutually agreed upon submittal time. The schedule may be a critical path method (CPM) schedule, bar chart, or other standard schedule format. Regardless of which format used, the schedule shall identify the critical path. The Engineer will evaluate the Type A Progress Schedule and approve or return the schedule for corrections within 15 calendar days of receiving the submittal.

1-08.4 Prosecution of Work **(July 23, 2015 APWA GSP)**

Delete this section in its entirety, and replace it with the following:

1-08.4 Notice to Proceed and Prosecution of Work

Notice to Proceed will be given after the contract has been executed and the contract bond and evidence of insurance have been approved and filed by the Contracting Agency. The Contractor shall not commence with the work until the Notice to Proceed has been given by the Engineer. The Contractor shall commence construction activities on the project site within ten days of the Notice to Proceed Date, unless otherwise approved in writing. The Contractor shall diligently pursue the work to the physical completion date within the time specified in the contract. Voluntary shutdown or slowing of operations by the Contractor shall not relieve the Contractor of the responsibility to complete the work within the time(s) specified in the contract.

When shown in the Plans, the first order of work shall be the installation of high visibility fencing to delineate all areas for protection or restoration, as described in the Contract. Installation of high visibility fencing adjacent to the roadway shall occur after the placement of all necessary signs and traffic control devices in accordance with 1-10.1(2). Upon construction of the fencing, the Contractor shall request the Engineer to inspect the fence. No other work shall be performed on the site until the Contracting Agency has accepted the installation of high visibility fencing, as described in the Contract.

1-08.4(1) Order Of Work **(*****)**

Add the following new section:

Prior to starting construction and issuance of notice to proceed by the City, the Contractor shall furnish the Contracting Agency with a schedule, sequence, and method of proceeding with the work. This schedule shall address all items herein and must be approved by the Contracting Agency prior to commencing any construction operations.

The following specific requirements shall be included into the project schedule:

- The removal of existing kennels may not begin until materials for proposed kennels are in the Contractor's possession and work may proceed without interruption.

1-08.5 Time for Completion **(March 13, 1995 WSDOT GSP 1-08.5OPT7.FR1)**

This project shall be physically completed within 60 working days.

1-08.5 Time for Completion **(December 30, 2022 APWA GSP Option A)**

Revise the third and fourth paragraphs to read:

Contract time shall begin on the first working day following the Notice to Proceed Date.

Each working day shall be charged to the contract as it occurs, until the contract work is physically complete. If Substantial Completion has been granted and all the authorized working days have been used, charging of working days will cease. Each week the Engineer will provide the Contractor a statement that shows the number of working days: (1) charged to the contract the week before; (2) specified for the Physical Completion of the contract; and (3) remaining for the Physical Completion of the contract. The statement will also show the nonworking days and any partial or whole day the Engineer declares as unworkable. The statement will be identified as a Written Determination by the Engineer. If the Contractor does not agree with the Written Determination of working days, the Contractor shall pursue the protest procedures in accordance with Section 1-04.5. By failing to follow the procedures of Section 1-04.5, the Contractor shall be deemed as having accepted the statement as correct. If the Contractor is approved to work 10 hours a day and 4 days a week (a 4-10 schedule) and the fifth day of the week in which a 4-10 shift is worked would ordinarily be charged as a working day then the fifth day of that week will be charged as a working day whether or not the Contractor works on that day.

Revise the sixth paragraph to read:

The Engineer will give the Contractor written notice of the Completion Date of the Contract after all the Contractor's obligations under the Contract have been performed by the Contractor. The following events must occur before the Completion Date can be established:

1. The physical Work on the project must be complete; and
2. The Contractor must furnish all documentation required by the Contract and required by law, to allow the Contracting Agency to process final acceptance of the contract. The following documents must be received by the Project Engineer prior to establishing a Completion Date:
 - a. Certified Payrolls (per Section 1-07.9(5)).
 - b. Material Acceptance Certification Documents
 - c. Monthly Reports of Amounts Credited as DBE Participation, as required by the Contract Provisions.
 - d. Final Contract Voucher Certification
 - e. Copies of the approved "Affidavit of Prevailing Wages Paid" for the Contractor and all Subcontractors
 - f. A copy of the Notice of Termination sent to the Washington State Department of Ecology (Ecology); the elapse of 30 calendar days from the date of receipt of the Notice of Termination by Ecology; and no rejection of the Notice of Termination by Ecology. This requirement will not apply if the Construction Stormwater General Permit is transferred back to the Contracting Agency in accordance with Section 8-01.3(16).
 - g. Property owner releases per Section 1-07.24

1-08.6 Suspension of Work **(February 15, 2023 Lacey GSP)**

Contract time may be suspended for procurement of critical materials (Procurement Suspension). In order to receive a Procurement Suspension, the Contractor shall within 40 calendar days after execution by the Contracting Agency, place purchase orders for all materials deemed critical by the Contracting Agency for physical completion of the contract. The Contractor shall provide copies of purchase orders for the critical materials. Such purchase orders shall disclose the purchase order date and estimated delivery dates for such critical material.

The Contractor shall show procurement of the materials anticipated to be critical materials as activities in the Progress Schedule. If approved Progress Schedule indicates that the materials procurement are critical activities, and if the Contractor has provided documentation that purchase orders are placed for the critical materials within the prescribed 21 calendar days, then contract time will be suspended upon physical completion of all critical work except that work dependent upon the critical materials. Items anticipated to be critical materials include but are not limited to:

Kennel components (bases, side panels, back panels, doors, etc.)

Charging of contract time will resume upon delivery of the critical materials to the Contractor or 365 calendar days, whichever occurs first except as approved by the Engineer.

1-08.9 Liquidated Damages **(March 3, 2021 APWA GSP, Option B)**

Revise the second and third paragraphs to read:

Accordingly, the Contractor agrees:

1. To pay (according to the following formula) liquidated damages for each working day beyond the number of working days established for Physical Completion, and
2. To authorize the Engineer to deduct these liquidated damages from any money due or coming due to the Contractor.

Liquidated Damages Formula

$$LD=0.15C/T$$

Where:

LD = liquidated damages per working day (rounded to the nearest dollar)

C = original Contract amount

T = original time for Physical Completion

When the Contract Work has progressed to Substantial Completion as defined in the Contract, the Engineer may determine the Contract Work is Substantially Complete. The Engineer will notify the Contractor in writing of the Substantial Completion Date. For overruns in Contract time occurring after the date so established, the formula for liquidated damages shown above will not apply. For overruns in Contract time occurring after the Substantial Completion Date, liquidated damages shall be assessed on the basis of direct engineering and related costs assignable to the project until the actual Physical Completion Date of all the Contract Work. The Contractor shall complete the remaining Work as promptly as possible. Upon request by the Project Engineer, the Contractor shall furnish a written schedule for completing the physical Work on the Contract.

1-09 MEASUREMENT AND PAYMENT

1-09.6 Force Account **(October 10, 2008 APWA GSP)**

Supplement this section with the following:

The Contracting Agency has estimated and included in the Proposal, dollar amounts for all items to be paid per force account, only to provide a common proposal for Bidders. All such dollar amounts are to become a part of Contractor's total bid. However, the Contracting Agency does not warrant expressly or by implication, that the actual amount of work will correspond with those estimates. Payment will be made on the basis of the amount of work actually authorized by Engineer.

1-09.7 Mobilization

(December 30, 2022 APWA GSP)

Delete this Section and replace it with the following:

Mobilization consists of preconstruction expenses and the costs of preparatory Work and operations performed by the Contractor which occur before 10 percent of the total original amount of an individual Bid Schedule is earned from other Contract items on that Bid Schedule. Items which are not to be included in the item of Mobilization include but are not limited to:

1. Any portion of the Work covered by the specific Contract item or incidental Work which is to be included in a Contract item or items.
2. Profit, interest on borrowed money, overhead, or management costs.
3. Any costs of mobilizing equipment for force account Work.

Based on the lump sum Contract price for "Mobilization", partial payments will be made as follows:

1. When 5 percent of the total original Bid Schedule amount is earned from other Contract items on that original Bid Schedule, excluding amounts paid for materials on hand, 50 percent of the Bid Item for mobilization on that original Bid Schedule, 5 percent of the total of that original Bid Schedule, or 5 percent of the total original Contract amount, whichever is the least, will be paid.
2. When 10 percent of the total original Bid Schedule amount is earned from other Contract items on that original Bid Schedule, excluding amounts paid for materials on hand, 100 percent of the Bid Item for mobilization on that original Bid Schedule, 10 percent of the total of that original Bid Schedule, or 10 percent of the total original Contract amount, whichever is the least, will be paid.
3. When the Substantial Completion Date has been established for the project, payment of any remaining amount Bid for mobilization will be paid.

Nothing herein shall be construed to limit or preclude partial payments otherwise provided by the Contract.

1-09.9 Payments

(December 30, 2022 APWA GSP)

Section 1-09.9 is revised to read:

The basis of payment will be the actual quantities of Work performed according to the Contract and as specified for payment.

The Contractor shall submit a breakdown of the cost of lump sum bid items at the Preconstruction Conference, to enable the Project Engineer to determine the Work performed on a monthly basis. A breakdown is not required for lump sum items that include a basis for incremental payments as part of the respective Specification. Absent a lump sum breakdown, the Project Engineer will make a determination based on information available. The Project Engineer's determination of the cost of work shall be final.

Progress payments for completed work and material on hand will be based upon progress estimates prepared by the Engineer. A progress estimate cutoff date will be established at the preconstruction conference.

The initial progress estimate will be made not later than 30 days after the Contractor commences the work, and successive progress estimates will be made every month thereafter until the Completion Date. Progress estimates made during progress of the work are tentative, and made only for the purpose of determining progress payments. The progress estimates are subject to change at any time prior to the calculation of the final payment.

The value of the progress estimate will be the sum of the following:

1. Unit Price Items in the Bid Form — the approximate quantity of acceptable units of work completed multiplied by the unit price.
2. Lump Sum Items in the Bid Form — based on the approved Contractor's lump sum breakdown for that item, or absent such a breakdown, based on the Engineer's determination.
3. Materials on Hand — 100 percent of invoiced cost of material delivered to Job site or other storage area approved by the Engineer.
4. Change Orders — entitlement for approved extra cost or completed extra work as determined by the Engineer.

Progress payments will be made in accordance with the progress estimate less:

1. Retainage per Section 1-09.9(1), on non FHWA-funded projects;
2. The amount of progress payments previously made; and
3. Funds withheld by the Contracting Agency for disbursement in accordance with the Contract Documents.

Progress payments for work performed shall not be evidence of acceptable performance or an admission by the Contracting Agency that any work has been satisfactorily completed. The determination of payments under the contract will be final in accordance with Section 1-05.1.

Failure to perform obligations under the Contract by the Contractor may be decreed by the Contracting Agency to be adequate reason for withholding any payments until compliance is achieved.

Upon completion of all Work and after final inspection (Section 1-05.11), the amount due the Contractor under the Contract will be paid based upon the final estimate made by the Engineer and presentation of a Final Contract Voucher Certification to be signed by the Contractor. The Contractor's signature on such voucher shall be deemed a release of all claims of the Contractor unless a Certified Claim is filed in accordance with the requirements of Section 1-09.11 and is expressly excepted from the Contractor's certification on the Final Contract Voucher Certification. The date the Contracting Agency signs the Final Contract Voucher Certification constitutes the final acceptance date (Section 1-05.12).

If the Contractor fails, refuses, or is unable to sign and return the Final Contract Voucher Certification or any other documentation required for completion and final acceptance of the Contract, the Contracting Agency reserves the right to establish a Completion Date (for the purpose of meeting the requirements of RCW 60.28) and unilaterally accept the Contract. Unilateral final acceptance will occur only after the Contractor has been provided the opportunity, by written request from the Engineer, to voluntarily submit such documents. If voluntary compliance is not achieved, formal notification of the impending establishment of a Completion Date and unilateral final acceptance will be provided by email with delivery confirmation from the Contracting Agency to the Contractor, which will provide 30 calendar days for the Contractor to submit the necessary documents. The 30 calendar day period will begin on the date the email with delivery confirmation is received by the Contractor. The date the Contracting Agency unilaterally signs the Final Contract Voucher Certification shall constitute the Completion Date and the final acceptance date (Section 1-05.12). The reservation by the Contracting Agency to unilaterally accept the Contract will apply to Contracts that are Physically Completed in accordance with Section 1-08.5, or

for Contracts that are terminated in accordance with Section 1-08.10. Unilateral final acceptance of the Contract by the Contracting Agency does not in any way relieve the Contractor of their responsibility to comply with all Federal, State, tribal, or local laws, ordinances, and regulations that affect the Work under the Contract.

Payment to the Contractor of partial estimates, final estimates, and retained percentages shall be subject to controlling laws.

1-09.9 Payments

(November 20, 2020 Lacey GSP)

Section 1-09.9 is supplemented with the following:

Progress payments and the Final Contract Voucher Certification (FCVC) will be transmitted electronically to the Contractor for signature. The Contractor shall apply all signatures electronically using the software provided by the Contracting Agency. Within 21 days of execution of the Contract, the Contractor shall submit the names, email addresses, and text-message capable phone numbers for the authorized signers and shall bear the name, phone number and email of the officer providing this authorization. Delegation of authority to sign progress payments and the FCVC shall be by the officer authorized to sign the Contract.

1-09.11(3) Time Limitation and Jurisdiction

(December 30, 2022 APWA GSP)

Revise this section to read:

For the convenience of the parties to the Contract it is mutually agreed by the parties that all claims or causes of action which the Contractor has against the Contracting Agency arising from the Contract shall be brought within 180 calendar days from the date of final acceptance (Section 1-05.12) of the Contract by the Contracting Agency; and it is further agreed that all such claims or causes of action shall be brought only in the Superior Court of the county where the Contracting Agency headquarters is located, provided that where an action is asserted against a county, RCW 36.01.050 shall control venue and jurisdiction. The parties understand and agree that the Contractor's failure to bring suit within the time period provided, shall be a complete bar to all such claims or causes of action. It is further mutually agreed by the parties that when claims or causes of action which the Contractor asserts against the Contracting Agency arising from the Contract are filed with the Contracting Agency or initiated in court, the Contractor shall permit the Contracting Agency to have timely access to all records deemed necessary by the Contracting Agency to assist in evaluating the claims or action.

1-09.13(1) General

(January 19, 2022 APWA GSP)

Revise this section to read:

Prior to seeking claims resolution through arbitration or litigation, the Contractor shall proceed in accordance with Sections 1-04.5 and 1-09.11. The provisions of Sections 1-04.5 and 1-09.11 must be complied with in full as a condition precedent to the Contractor's right to seek claim resolution through binding arbitration or litigation.

Any claims or causes of action which the Contractor has against the Contracting Agency arising from the Contract shall be resolved, as prescribed herein, through binding arbitration or litigation.

The Contractor and the Contracting Agency mutually agree that those claims or causes of action which total \$1,000,000 or less, which are not resolved by mediation, shall be resolved through litigation unless the parties mutually agree in writing to resolve the claim through binding arbitration.

The Contractor and the Contracting Agency mutually agree that those claims or causes of action in excess of \$1,000,000, which are not resolved by mediation, shall be resolved through litigation unless the parties mutually agree in writing to resolve the claim through binding arbitration.

1-09.13(3)A Arbitration General
(January 19, 2022 APWA GSP)

Revise the third paragraph to read:

The Contracting Agency and the Contractor mutually agree to be bound by the decision of the arbitrator, and judgment upon the award rendered by the arbitrator may be entered in the Superior Court of the county in which the Contracting Agency's headquarters is located, provided that where claims subject to arbitration are asserted against a county, RCW 36.01.050 shall control venue and jurisdiction of the Superior Court. The decision of the arbitrator and the specific basis for the decision shall be in writing. The arbitrator shall use the Contract as a basis for decisions.

1-09.13(4) Venue for Litigation
(December 30, 2022 APWA GSP)

Revise this section to read:

Litigation shall be brought in the Superior Court of the county in which the Contracting Agency's headquarters is located, provided that where claims are asserted against a county, RCW 36.01.050 shall control venue and jurisdiction of the Superior Court. It is mutually agreed by the parties that when litigation occurs, the Contractor shall permit the Contracting Agency to have timely access to all records deemed necessary by the Contracting Agency to assist in evaluating the claims or action.

8-50 MISCELLANEOUS

8-50.2 PROJECT CLOSEOUT
(April 2, 2018 Lacey GSP)

Description

This work shall consist of completing all miscellaneous items of work in accordance with the Plans and these Specifications that are required to achieve Completion and Final Acceptance, as identified by the Engineer and the Contracting Agency. This work may include but is not limited to punch list items, record drawings, O&M Manuals, training, material acceptance documents, copies of the approved "Affidavit of Prevailing Wages Paid" for the Contractor and all Subcontractors, and any other work required in these Plans and Specifications that has not been completed.

Measurement

No unit of measurement shall apply to the lump sum price for "Project Closeout".

Payment

"Project Closeout", lump sum.

The unit contract price per lump sum for "Project Closeout" includes all compensation for all costs of completing the miscellaneous items of work identified by the Contracting Agency prior to final acceptance of the Project. A fixed lump sum price has been included in the Proposal for this work. Any additional costs anticipated or incurred by the Contractor for the work shall be included in the various

lump sum and unit price bid items as found in the Proposal. Neither partial payment, nor additional compensation shall be allowed

8-51 BUILDING IMPROVEMENTS

(*****)

8-51.1 Description

This work shall consist of removal and disposal of the 18 existing kennels in the dog adoption room at the animal services building. This work shall also include furnishing and completely installing 18 new kennels in accordance with the Plans, Standard Plans, and these Specifications, at the locations shown in the Plans or as staked by the Engineer. Of the new kennels, at least 2 conjoining kennels will have top covers.

The Contractor can view the property by appointment only. Call Brett Boogerd at (360) 486-8732 to schedule an appointment.

8-51.2 Regulations and Code

All work shall conform to the standards of the international building code, international fire code, Washington State Energy Code, State and County Department of Health, Occupational Safety and Health Administration (OSHA), Washington Industrial Safety and Health Act (WISHA), National Fire Protection association (NFPA), and any WACs and local ordinances, whichever applicable.

The Code, rule, or standard shall be construed to mean the code, rule, or standard that is in effect on the Bid Opening date.

8-51.3 Materials

Materials shall meet the requirements of the following sections

Material for kennels shall conform with the specifications outlined in Section E or an approved equal.

Piping and fittings for drain lines shall conform to the following specifications:

1. Piping materials shall bear label, stamp, or other markings of specified testing agency.
2. Solid-Wall ABS Pipe: ASTM D2661, Schedule 40.
3. ABS Socket Fittings: ASTM D2661, made to ASTM D3311, drain, waste, and vent patterns.
4. 1/4" per foot slope

8-51.4 Construction Requirements

Work shall include protecting all existing materials intended to be kept in place, including but not limited to: flooring, plumbing, electrical fixtures, and wiring. Work shall also consist of removing and replacing any fixtures or other items as necessary to complete removal of existing kennels and installation of new kennels, including but not limited to: drain lines, existing copper lines for flushing drains. Materials shall be properly stored and handled to prevent damage and assure reliable performance.

Kennels shall be installed straight, plumb, level, in true alignment and securely anchored.

All workmanship shall be complete and in accordance with the latest accepted standards of the industry, including but not limited to the following:

- A. Install piping in concealed locations unless otherwise indicated and except in equipment rooms and service areas.
- B. Install piping free of sags and bends.
- C. Install fittings for changes in direction and branch connections.
- D. Make changes in direction for soil and waste drainage and vent piping using appropriate branches, bends, and long-sweep bends.
 - 1. Sanitary tees and short-sweep 1/4 bends may be used on vertical stacks if change in direction of flow is from horizontal to vertical.
 - 2. Use long-turn, double Y-branch and 1/8-bend fittings if two fixtures are installed back to back or side by side with common drain pipe.
 - a. Straight tees, elbows, and crosses may be used on vent lines.
 - 3. Do not change direction of flow more than 90 degrees.
 - 4. Use proper size of standard increasers and reducers if pipes of different sizes are connected.
 - a. Reducing size of waste piping in direction of flow is prohibited.
- E. Install soil and waste and vent piping at the following minimum slopes unless otherwise indicated:
 - 1. Building Sanitary Waste: 2 percent downward in direction of flow for piping NPS 3 (DN 80) and smaller; 1 percent downward in direction of flow for piping NPS 4 (DN 100) and larger.
 - 2. Horizontal Sanitary Waste Piping: 2 percent downward in direction of flow.
- F. Install aboveground ABS piping in accordance with ASTM D2661.
- G. Do not enclose, cover, or put piping into operation until it is inspected and approved by authorities having jurisdiction.
- H. Install hangers for ABS piping, with maximum horizontal spacing and minimum rod diameters, to comply with manufacturer's written instructions, locally enforced codes, and authorities having jurisdiction requirements, whichever are most stringent.

8-51.5 Measurement

Building improvements shall be paid for per lump sum regardless of the type, size and quantity of material used. A schedule of values shall be provided for removal of the existing kennels, installation of the new kennels, and other work.

8-51.6 Payment


Payment will be made in accordance with Section 1-04.1, for the following bid items:

All costs to comply with the permit requirements shall be incidental to the project and no other compensation will be allowed. Payment will be made as follows:

“Building Improvements,” lump sum.


The unit contract price per lump sum for “Building Improvements” shall be full pay for furnishing all labor, materials, tools, and equipment necessary to complete the work as shown in the plans and herein specified including but not limited to, restoring facilities destroyed or damaged during construction, salvaging existing materials, obtaining permits, and testing. All additional materials and labor, not shown in the plans or called for herein and which are required to complete the fully operational system, shall be included in the lump sum contract price.

APPENDIX A – COL RAM FORM & INSTRUCTIONS

PROJECT:		SUBMITTAL NO.		
LACEY CONTRACT NO. PW ____-20____		Date sent to City:		
Request for Approval of Material, Product or Shop Drawing				
Contractor:			Subcontractor:	
No. of Pages	Item: Material, Product or Shop Drawing			Specification Reference
<input type="checkbox"/> This item is as specified OR <input type="checkbox"/> This item is a substitution/or equal Material/Product Substitution Request shall be submitted				
<input type="checkbox"/> Supplier/Subcontractor certifies material/product conforms to contract.				
Review Priority: <input type="checkbox"/> 1 <input type="checkbox"/> 2 <input type="checkbox"/> 3 Requested Due Date:				
Notes to Engineer:				

City of Lacey Engineer:		Date Approved by City:	
<input type="checkbox"/> Rejected	New Submittal Required.		
<input type="checkbox"/> Revise and Resubmit	See Engineer's comments.		
<input type="checkbox"/> Conditionally Approved	See items included in Engineer's comments.		
<input type="checkbox"/> Conditionally Approved	No exceptions noted.		
Review of the materials, products or plans do not relieve the contractor from compliance with requirements of the contract documents and does not necessarily constitute acceptance for materials, products or plans to be incorporated in the work. This review is for general conformance of the project's conceptual design and general compliance with the project's plans and specifications.			
Date City Transmitted to Contractor:		Date Contractor Transmitted to Subcontractor/Supplier:	

Date Received by City of Lacey:	Reviewed by: (Name/Company)
<u>Engineer's Comments:</u> 1.	

PROJECT: <i>A</i>		SUBMITTAL NO. <i>C</i>	 CITY OF LACEY
LACEY CONTRACT NO. PW___-20___ <i>B</i>			
Request for Approval of Material, Product or Shop Drawing			
Contractor: <i>D</i>		Subcontractor: <i>E</i>	
No. of Pages	Item: Material, Product or Shop Drawing		Specification Reference
<i>F</i>	<i>G</i>		<i>H</i>
<input type="checkbox"/> This item is as specified <i>I1</i> OR <input type="checkbox"/> This item is a substitution/or equal Material/Product Substitution Request shall be submitted <i>I2</i>			
<input type="checkbox"/> Supplier/Subcontractor certifies material/product conforms to contract.			
Review Priority: <input type="checkbox"/> 1 <i>K</i> <input type="checkbox"/> 2 <input type="checkbox"/> 3 Requested Due Date: <i>L</i>			
Notes to Engineer: <i>M</i>			

Section 1

City of Lacey Engineer: <i>R</i>		Date City Transmitted to Contractor: <i>S</i>
<input type="checkbox"/> Rejected	New Submittal Required.	
<input type="checkbox"/> Revise and Resubmit	See Engineer's comments.	
<input type="checkbox"/> Conditionally Approved	See items included in Engineer's comments.	
<input type="checkbox"/> Conditionally Approved	No exceptions noted.	
Review of the materials, products or plans do not relieve the contractor from compliance with requirements of the contract documents and does not necessarily constitute acceptance for materials, products or plans to be incorporated in the work. This review is for general conformance of the project's conceptual design and general compliance with the project's plans and specifications.		
Date Received by Contractor: <i>T</i>		Date Returned to Subcontractor/Supplier: <i>U</i>

Section 3

Date Received by City of Lacey:	<i>N</i>	Reviewed by: (Name/Company)	<i>@</i>
------------------------------------	----------	--------------------------------	----------

Engineer's Comments:

1. *P*

Section 2

Section 1

The **Project Manager** shall fill in items **A** and **B**. The “Request for Approval of Material, Products or Shop Drawing” form shall be included in the specifications.

A Project Manager enters in the project title that matches the plans and specifications.

B Project Manager enters in PW project number that matches the plans and specifications.

The **Contractor** shall fill out the “Request for Approval of Material, Product or Shop Drawing” form for all materials or products that will be installed and Shop Drawing that will be used in the project. The form and the submittal shall be sent in the same e-mail. Submittals that exceed 10 MB shall either be provided on a CD, a flash drive or an internet link.

The products and materials that are specific to the project shall be circled or highlighted. If a submittal includes products or materials that are not project specific then these items shall be crossed out. Project Submittals that exceed 10 pages shall be submitted in Adobe Acrobat format and include a table of contents. Submittals that are not submitted in this format may be rejected outright and the contractor will be required to resubmit in the correct format.

The contractor shall enter in items **C, D, E, F, G, H, I, J, K, L**, and **M**.

C Contractor enters in the submittal number. The first “Request for Approval of Material, Product or Shop Drawing” submittal number shall be 1.0, the second shall be 2.0, the third shall be 3.0, etc.

When a “Request for Approval of Material, Product or Shop Drawing” requires resubmitting, the next submittal shall be the first part of the submittal number and then 0.1. Example: If submittal 9.0 requires resubmitting, then the resubmittal shall be 9.1. If a second resubmittal is required, then the next resubmittal shall be 9.2.

D Contractor shall fill in their name.

E Contractor shall fill in the subcontractor that is requesting approval. If only the General Contractor is requesting approval, then NA (not applicable) shall be entered.

F The number of pages for each specific material, product or shop drawing shall be entered.

G The specific material, product or shop drawing shall be entered. Material or product will be the trade name of the product or the name it is most easily recognized by. Materials or products that are similar (i.e. pipe fittings) can be bundled into one submittal.

H The specification that pertains to the specific material, product or shop drawing shall be entered. This information is critical in comparing the material, product or shop drawing to the specifications. You may also list Plan Sheet number or Special Provision page in this area.

I The Contractor shall check if the items submitted are either specified (I1) or that the submitted item is a substitution or equal (I2). If the product is a substitute or equal, then a Material/Product Substitution Request shall be submitted.

J The Contractor shall check that supplier and/or subcontractor certifies the bid item.

K The Contractor shall check if the submittal for approval is a high (1), average (2) or low (3) priority. The City of Lacey will review priority submittals as quickly as possible. Note: The majority of the submittals shall be checked as priority 2 or 3. Priority 1 submittals shall be critical or long lead items.

L A due date can be entered by the contractor. The City of Lacey will endeavor to review and return the request for approval by the requested due date.

M Any additional notes that the Contractor finds would assist the City of Lacey in reviewing the submittal can be entered in here.

Section 2

The **City of Lacey Engineer** shall fill in items **N**, **O** and **P**.

N Enter the date that the City of Lacey received the “Request for Approval of Material, Product or Shop Drawing” from the Contractor.

O Enter the name and company of the person that reviewed the submittal.

P Any comments regarding changes needed, resubmittals requirements, conditional approval, etc. shall be entered.

Section 3

The **City of Lacey Engineer** shall fill in items **Q**, **R**, and **S**.

Q Either “Rejected: New Submittal Required.”, “Review and Resubmit: See Engineer’s comments.”, “Conditionally Approved: See items included in Engineer’s comments.”, or “Conditionally Approved: No exceptions noted” shall be checked”.

R Enter the name of the Engineer sending the submittal back to the Contractor. The Engineering sending the form back may not necessarily be the Engineer completing the review.

S Enter the date that the City of Lacey transmits the “Request for Approval of Material, Product or Shop Drawing” to the Contractor.


The **Contractor** shall enter in items **T** and **U** for their own records. If there is a discrepancy between the **S** “Date City Transmitted to Contractor” and **T**, the Contractor shall notify the City of Lacey within 3 working days.

T Contractor enters the date that they received the completed “Request for Approval of Material or Shop Drawing”.

U Contractor enters the date that that they return the completed “Request for Approval of Material or Shop Drawing” to the Subcontractor/Supplier.


APPENDIX B – PLANS AND AS-BUILTS

PROPOSED CONFIGURATION

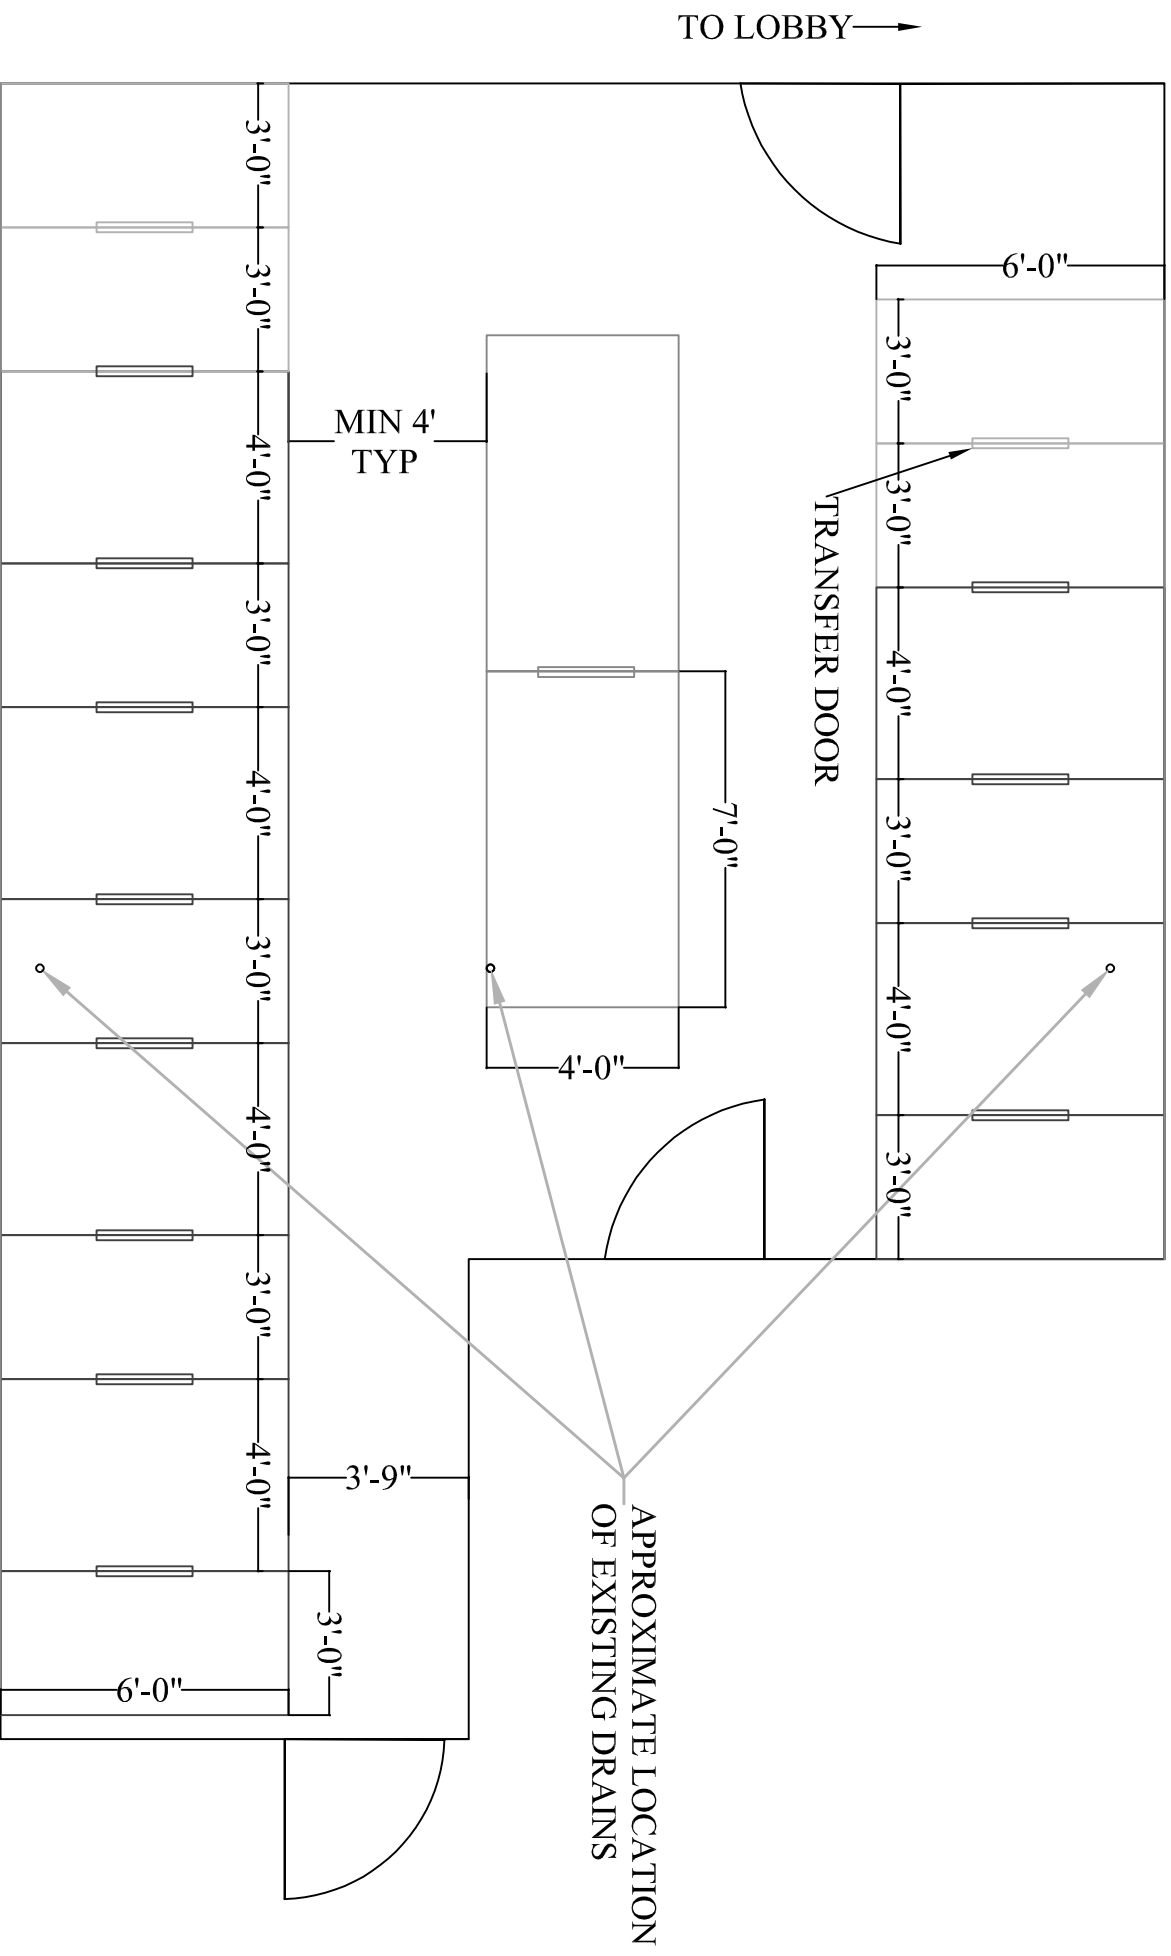

EXISTING CONFIGURATION

TO LOBBY →

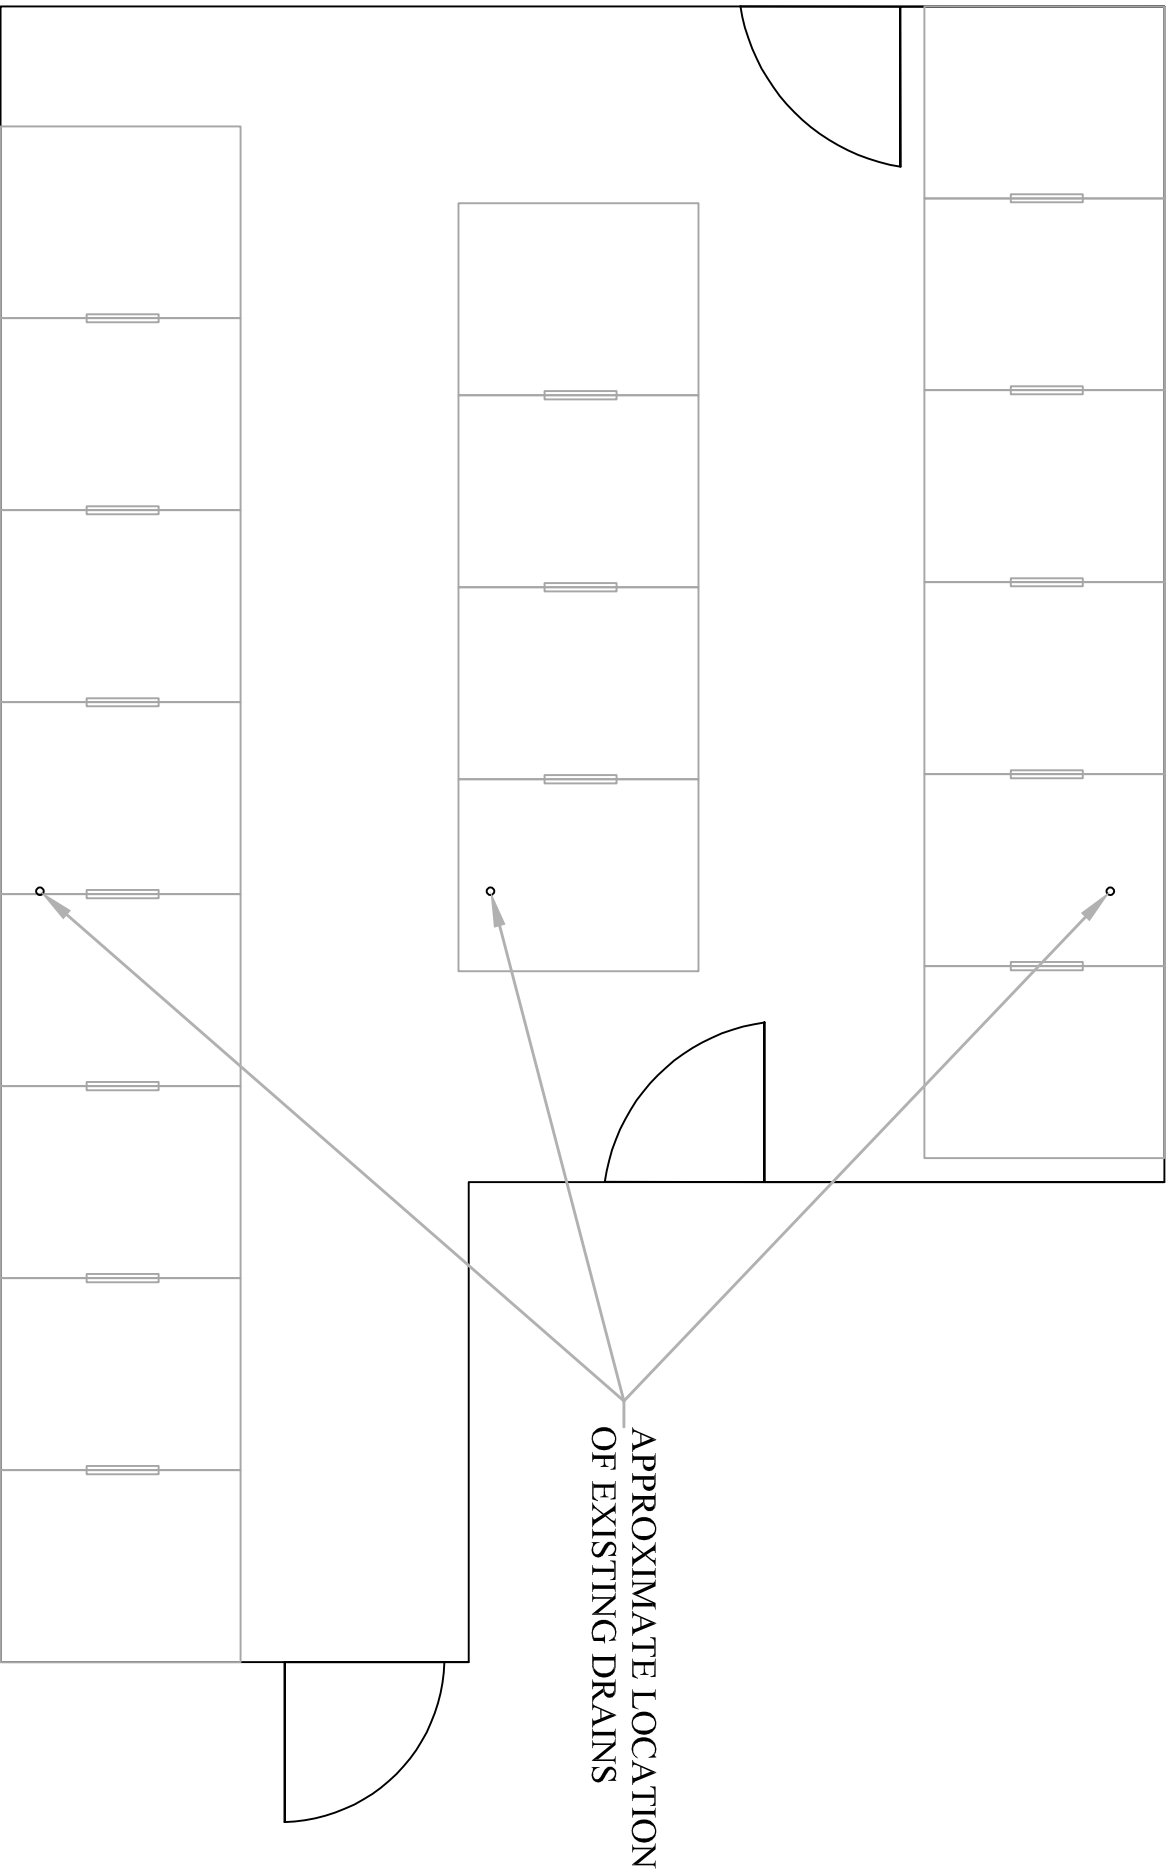

Architectural floor plan of a building. A blue rectangle highlights a specific area in the lower-left quadrant. A blue arrow points to the bottom-left corner of this rectangle. The plan includes various rooms and areas, such as 'COOLING TOWER', 'ELECTRICAL', 'MECHANICAL', 'PUMP ROOM', 'ELEVATOR', 'STAIRS', and 'OFFICE'. It also shows structural elements like columns and beams, and is labeled with dimensions and room numbers. The plan is oriented with North at the top.

[illegible]

PROJECT AREA


REMODEL OF AN
EXISTING BUILDING
TO CREATE AN
ANIMAL SHELTER

CITY OF LACEY
ON BEHALF OF
ANIMAL SERVICES


PLUMBING PLAN

Print Date 5/22/19

21

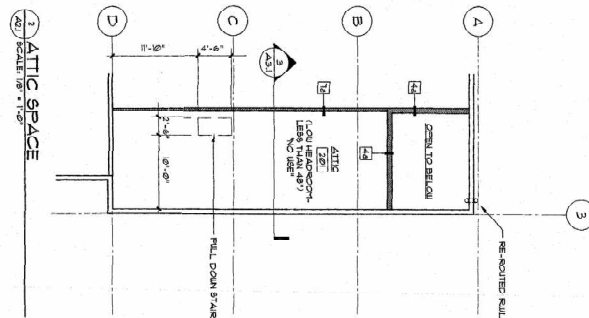


1 ATTIC SPACE
SCALE: 1/8" = 1'-0"

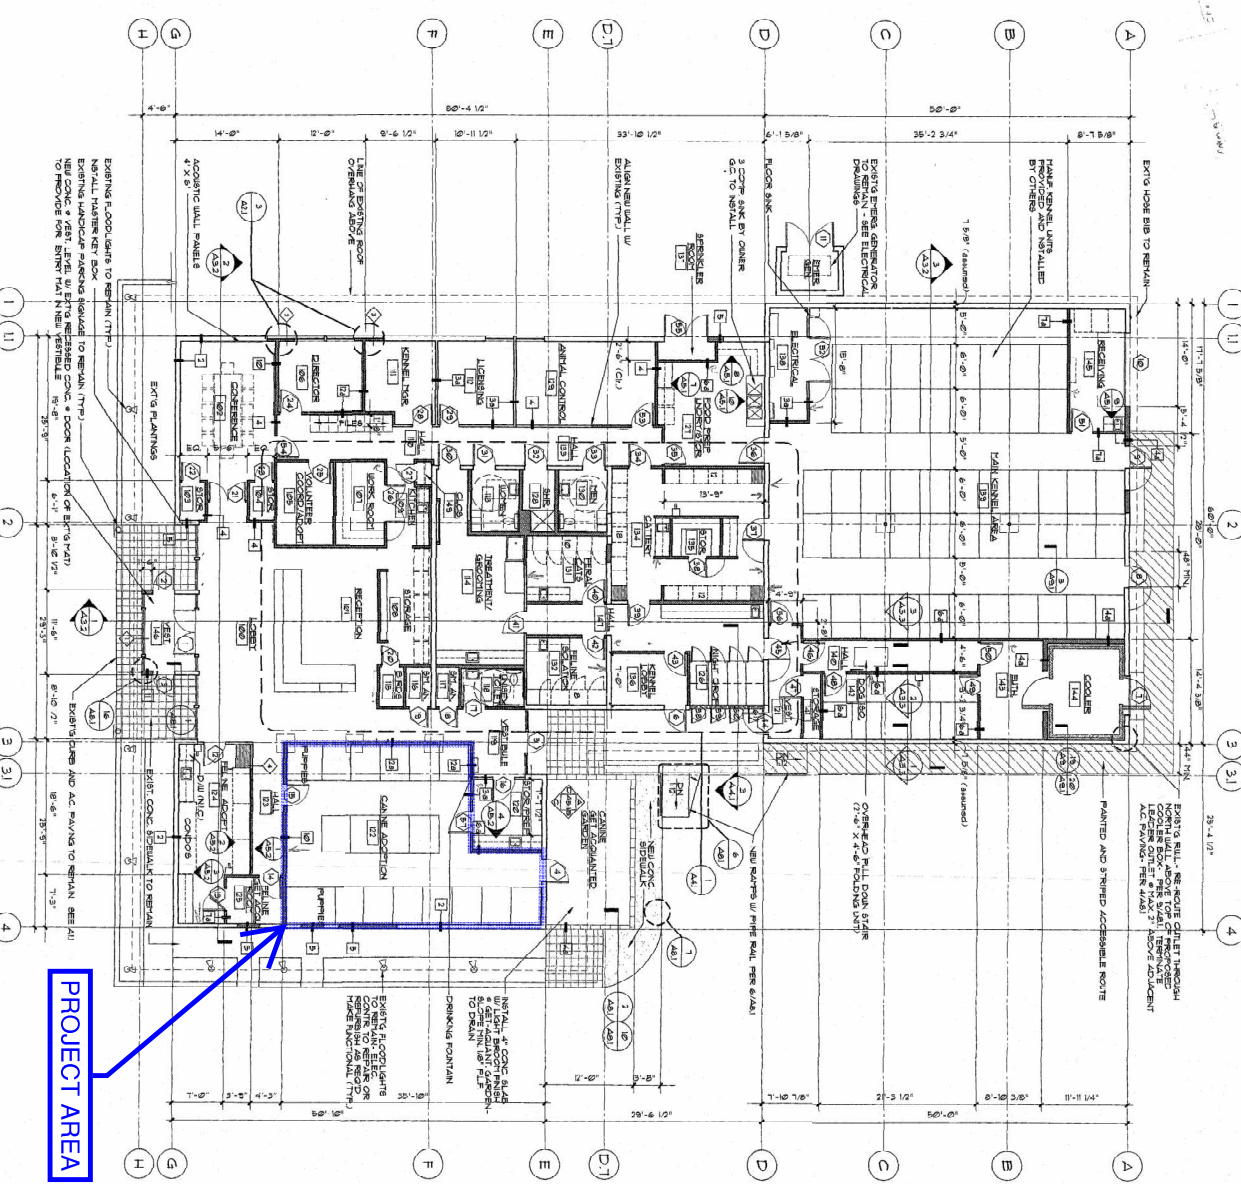

2 FLOOR PLAN
SCALE: 1/8" = 1'-0"

3 WINDOW INFILL DETAIL
SCALE: 1/4" = 1'-0"

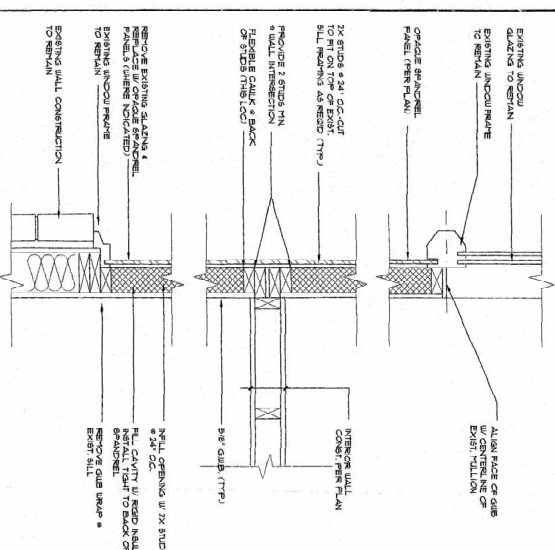

PROJECT AREA

FLOOR PLANS

Legend

No.	Description
1	EXISTING FLOOR LIFT TO REMAIN (TYP)
2	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
3	PAINTED AND STRIPED ACCESSIBLE ROUTE
4	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
5	NEW STAIRS W/ PRIME BAL. (PER ADA)
6	EXISTING FLOOR LIFT TO REMAIN (TYP)
7	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
8	PAINTED AND STRIPED ACCESSIBLE ROUTE
9	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
10	NEW STAIRS W/ PRIME BAL. (PER ADA)
11	EXISTING FLOOR LIFT TO REMAIN (TYP)
12	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
13	PAINTED AND STRIPED ACCESSIBLE ROUTE
14	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
15	NEW STAIRS W/ PRIME BAL. (PER ADA)
16	EXISTING FLOOR LIFT TO REMAIN (TYP)
17	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
18	PAINTED AND STRIPED ACCESSIBLE ROUTE
19	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
20	NEW STAIRS W/ PRIME BAL. (PER ADA)
21	EXISTING FLOOR LIFT TO REMAIN (TYP)
22	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
23	PAINTED AND STRIPED ACCESSIBLE ROUTE
24	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
25	NEW STAIRS W/ PRIME BAL. (PER ADA)
26	EXISTING FLOOR LIFT TO REMAIN (TYP)
27	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
28	PAINTED AND STRIPED ACCESSIBLE ROUTE
29	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
30	NEW STAIRS W/ PRIME BAL. (PER ADA)
31	EXISTING FLOOR LIFT TO REMAIN (TYP)
32	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
33	PAINTED AND STRIPED ACCESSIBLE ROUTE
34	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
35	NEW STAIRS W/ PRIME BAL. (PER ADA)
36	EXISTING FLOOR LIFT TO REMAIN (TYP)
37	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
38	PAINTED AND STRIPED ACCESSIBLE ROUTE
39	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
40	NEW STAIRS W/ PRIME BAL. (PER ADA)
41	EXISTING FLOOR LIFT TO REMAIN (TYP)
42	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
43	PAINTED AND STRIPED ACCESSIBLE ROUTE
44	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
45	NEW STAIRS W/ PRIME BAL. (PER ADA)
46	EXISTING FLOOR LIFT TO REMAIN (TYP)
47	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
48	PAINTED AND STRIPED ACCESSIBLE ROUTE
49	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
50	NEW STAIRS W/ PRIME BAL. (PER ADA)
51	EXISTING FLOOR LIFT TO REMAIN (TYP)
52	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
53	PAINTED AND STRIPED ACCESSIBLE ROUTE
54	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
55	NEW STAIRS W/ PRIME BAL. (PER ADA)
56	EXISTING FLOOR LIFT TO REMAIN (TYP)
57	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
58	PAINTED AND STRIPED ACCESSIBLE ROUTE
59	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
60	NEW STAIRS W/ PRIME BAL. (PER ADA)
61	EXISTING FLOOR LIFT TO REMAIN (TYP)
62	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
63	PAINTED AND STRIPED ACCESSIBLE ROUTE
64	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
65	NEW STAIRS W/ PRIME BAL. (PER ADA)
66	EXISTING FLOOR LIFT TO REMAIN (TYP)
67	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
68	PAINTED AND STRIPED ACCESSIBLE ROUTE
69	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
70	NEW STAIRS W/ PRIME BAL. (PER ADA)
71	EXISTING FLOOR LIFT TO REMAIN (TYP)
72	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
73	PAINTED AND STRIPED ACCESSIBLE ROUTE
74	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
75	NEW STAIRS W/ PRIME BAL. (PER ADA)
76	EXISTING FLOOR LIFT TO REMAIN (TYP)
77	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
78	PAINTED AND STRIPED ACCESSIBLE ROUTE
79	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
80	NEW STAIRS W/ PRIME BAL. (PER ADA)
81	EXISTING FLOOR LIFT TO REMAIN (TYP)
82	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
83	PAINTED AND STRIPED ACCESSIBLE ROUTE
84	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
85	NEW STAIRS W/ PRIME BAL. (PER ADA)
86	EXISTING FLOOR LIFT TO REMAIN (TYP)
87	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
88	PAINTED AND STRIPED ACCESSIBLE ROUTE
89	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
90	NEW STAIRS W/ PRIME BAL. (PER ADA)
91	EXISTING FLOOR LIFT TO REMAIN (TYP)
92	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
93	PAINTED AND STRIPED ACCESSIBLE ROUTE
94	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
95	NEW STAIRS W/ PRIME BAL. (PER ADA)
96	EXISTING FLOOR LIFT TO REMAIN (TYP)
97	NEW COINC. & VENT. LEVEL W/ EXIST. RECESSED COINC. & POOR LOCATION OF EXIST. VENT.
98	PAINTED AND STRIPED ACCESSIBLE ROUTE
99	OVERHEAD ROLL DOWN STAIR (7'-0" X 4'-0" FOLDING UNIT)
100	NEW STAIRS W/ PRIME BAL. (PER ADA)

Project

REMODEL OF AN EXISTING BUILDING TO CREATE AN ANIMAL SHELTER

**300 NORTH 1ST AVE
CLARK, NJ**

Client

**CITY OF LACEY
ON BEHALF OF
ANIMAL SERVICES**

Design Team

Architect
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.

Engineer
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.

Contractor
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.

Checklist
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.


Approval
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.



Scale
SHEPARD EKINS ARCHITECTS INCORPORATED, P.S.



Sheet No.
A 21

APPENDIX C – SITE PHOTOS



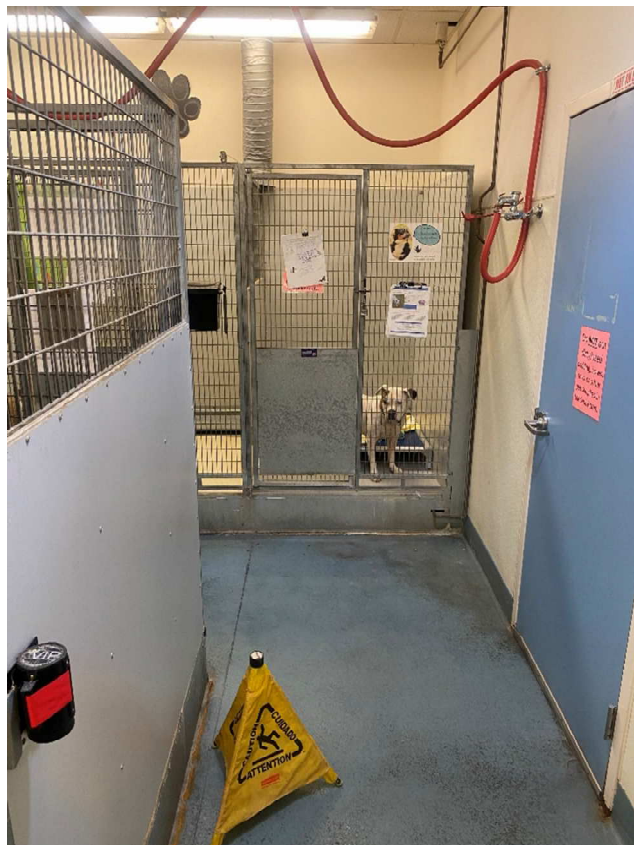

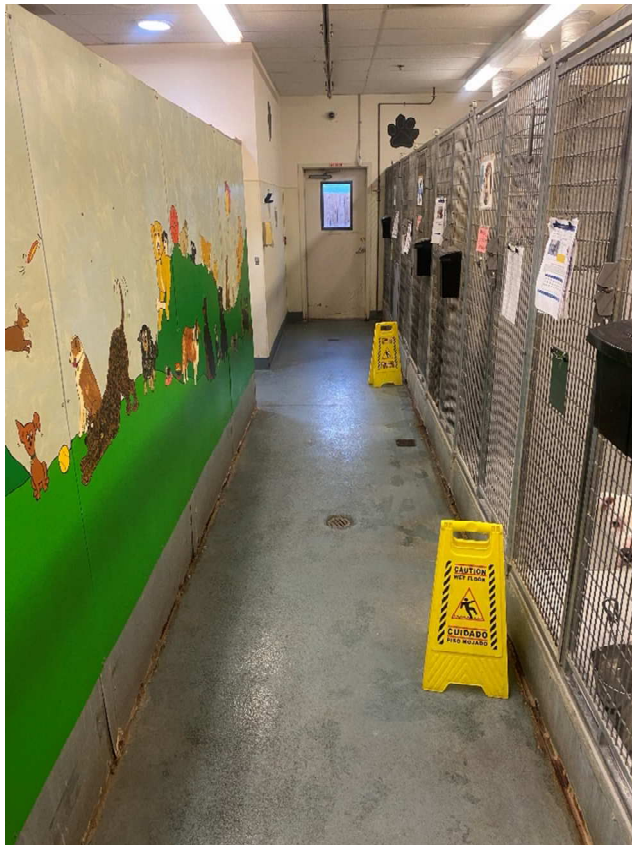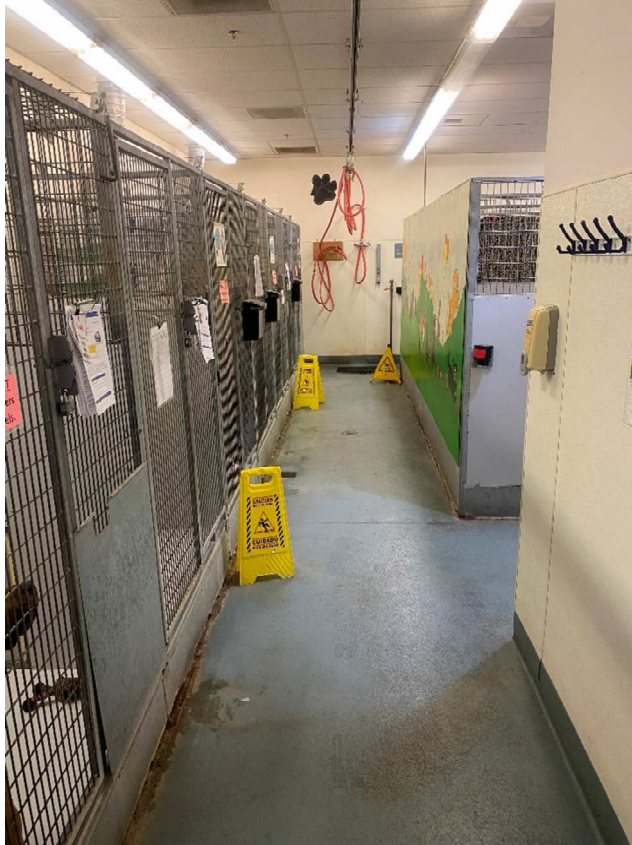

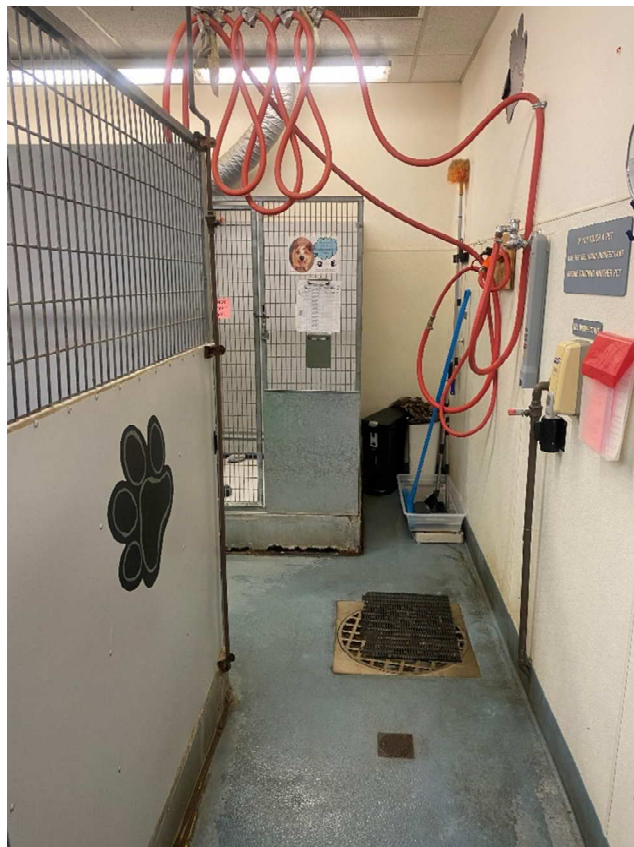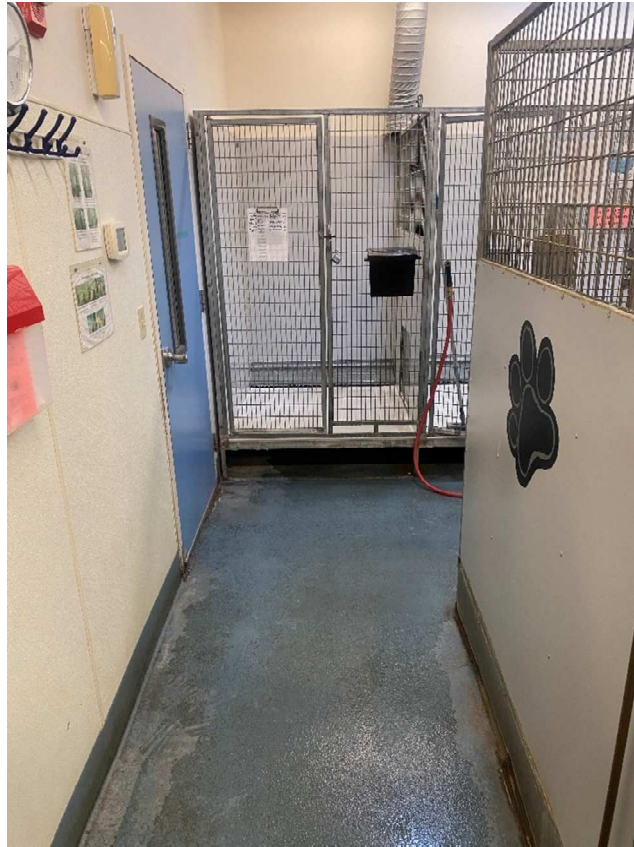





EXISTING CONFIGURATION OF DRAIN 1




EXISTING CONFIGURATION OF DRAIN 1




EXISTING CONFIGURATION OF DRAIN 2



EXISTING CONFIGURATION OF DRAIN 2

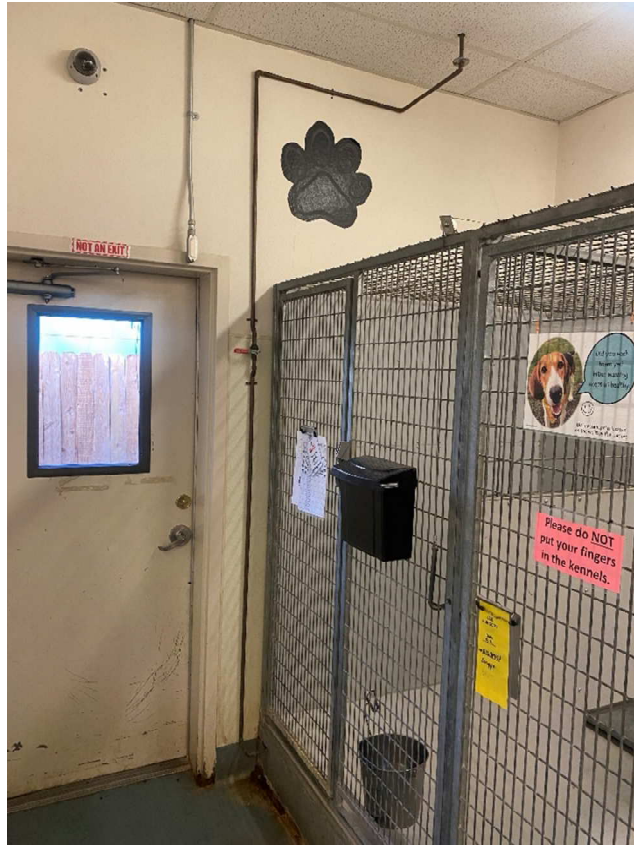

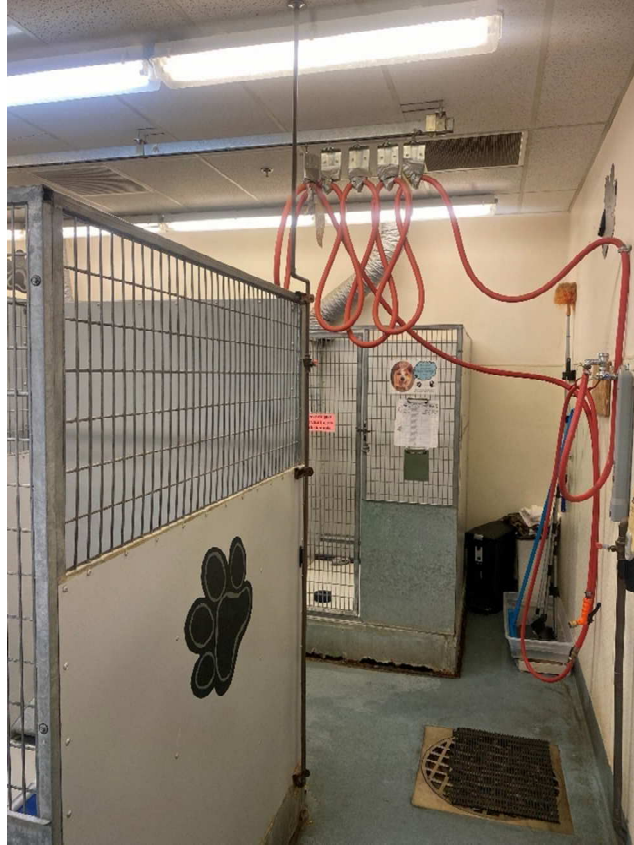

E

Technical Specifications

Ultrabase™ Above Floor System

Base unit shall be constructed of molded, solid surface Lite-Gran® fiberglass-reinforced plastic with a 1/2" thick honeycomb core in the main floor area. The base unit shall contain a 2" PVC drain with removable snap-in hair guard. 3/4" plywood pads covered by fiberglass-reinforced plastic shall be molded into each corner of the underside of the base unit.

UltraBase™ legs shall be Super Gatorshield™ ASTM A500 structural steel tubing, threaded at one end and having a threaded insert at the opposite end. Four stainless steel bolts with lock nuts and adjustable floor pads shall be provided for insertion into each threaded insert to provide a means for leveling the base units. Units shall have molded ledges on each side to provide a secure mounting position for (optional) resting bench.

ALUMINUM FRAMED FRP ISOLATION PANELS

Panels shall be constructed of an outer framework of 6063-T52 aluminum U-channel 3/4" x 3/4" x 1/8" thick. Internal braces shall be 6061-T6 aluminum H-channels 1-1/2" x 3/4" x 1/8" thick.

Bottom portion of isolation panel shall be one of the following materials:

1. .030" FRP bonded on each side of a .400" HDPE substrate. Solid panels to be perimeter sealed to the aluminum framework to a height of 4'.
2. High pressure Wilsonart® laminate bonded on each side of a .400" HDPE substrate (specify height). Solid panels to be perimeter sealed to the aluminum framework to a height of 4'.
3. 24 gauge (.024") 304 stainless steel sheet bonded on each side of a .400" HDPE substrate (specify height). Solid panels to be perimeter sealed to the aluminum framework to a height of 4'.

Upper portion shall be one of the following materials:

1" grid polyethylene structural foam 7/16" thick to a height of 4'.

1. .030" FRP bonded on each side of a .400" HDPE substrate to a height of 4'. Solid panels to be perimeter sealed to the aluminum framework (specify height).
2. High pressure Wilsonart® laminate bonded on each side of a .400" HDPE substrate to a height of 4'. Solid panels to be perimeter sealed to the aluminum framework (specify height).
3. 24 gauge (.024") 304 stainless steel sheet bonded on each side of a .400" HDPE substrate to a height of 4'. Solid panels to be perimeter sealed to the aluminum framework.
4. Stainless steel welded wire. Wire panels shall be welded at each juncture and shall consist of either 1/8" or 3/16" diameter vertical wires with 1 1/2" spacing between wires and 1/4" or 3/16" diameter horizontal wires with 4 1/4" spacing between wires. Wire panels shall be contained by means of a semi-rigid PVC extrusion inset into the aluminum framework.
5. Glass panels shall be 1/4" tempered glass held in place by a semi-rigid PVC extrusion inset into the aluminum framework.

STAINLESS STEEL GATES AND STALL FRONTS

Gate and stall front frames shall consist of 1" x 1 1/2" gauge (.060" wall) square 304 A-554 welded stainless steel tubing with 180 grit polish. Each corner of the frame shall be TIG welded.

Gate grids shall be constructed of 304 stainless steel wire 3/16" in diameter in the vertical direction with 15/16" spacing between wires, and 304 stainless steel wire 3/16" in diameter in the horizontal direction with 3-5/8" or less spacing between wires.

Horizontal and vertical wires shall be resistance welded at each juncture and each wire shall insert into the framework.

Gate Hinges shall consist of two 3/8" diameter stainless steel hex head screws which shall be threaded into stainless steel tapped plugs inserted into the top and bottom of the door frame. Each plug shall contain a nylon pivot bushing for smooth precision rotation.

Patented stainless steel two-way latch shall open both outward and inward. The latch shall secure automatically when gate is closed from the outward position and from the inward position it shall be able to latch and open from the inside of kennel. It shall be designed to accept a padlock. The two-way latch bar, the latch catch, and the swing pendant shall be made from 304 stainless steel.

3' height Solid internal panels shall be 1/2" FRP framed in an outer framework of 6063-T52 aluminum U-channel 3/4" x 3/4" x 1/8" thick. Panels shall be secured to the frame by means of stainless steel fasteners.

STAINLESS STEEL TOP COVERS

Perimeter frame and internal bracing shall consist of 1" x 1 1/2" gauge (.065" wall) square 304 A-554 welded stainless steel tubing with 180 grit polish. Each corner of the frame shall be TIG welded.

Wire grids shall be constructed of 304 stainless steel wire 1/8" in diameter in both directions with 3" spacing between wire centerlines. All wires shall be resistance welded at each juncture. Wire grid shall be TIG welded securely to the square tubing framework.

Transfer Doors

Vertical sliding doors shall be one of the following materials (specify, #1, #2, #3):

1. 1/4" thick, low-stress translucent polypropylene.
2. 1/4" thick Polymetal.
3. 0.100" thick Aluminum.

Channels shall be solid extruded aluminum 6063-T6. Doors are raised or lowered by pulling or releasing a 3/32" stainless steel wire cable that is secured to the top of the door. Transfer doors come equipped with cable, "S" hooks, pulleys, screw-eyes, and all necessary hardware for easy installation.

Transfer doors have openings 34" high x 17" wide. Optional cable guards shall be made of 0.100" aluminum sheet and shall be fastened to the channels with stainless steel screws.

F PREVAILING WAGES

PREVAILING WAGE RATES

The following wage rates are in effect for this project.

**State of Washington
Department of Labor and Industries
Washington State Prevailing Wage Rates For Public Works Contracts**

Thurston County Rates For All Trades

**Effective: August 30, 2023 including any correction notices issued
by Labor and Industries prior to bid.**

Wage Rates and the Benefit Code Key may be found at:
<https://secure.lni.wa.gov/wagelookup/>

Supplemental to State Wage Rates may be found at:
<http://www.wsdot.wa.gov/Design/ProjectDev/WageRates/default.htm>

A copy is also available for viewing at the City of Lacey Public Works Engineering office located at 420 College St SE, Lacey, WA 98503. If requested, a hard copy will be mailed to you.
